



Roads &  
Maritime

Roads and Maritime Services

BRIEF COMPRISING OF THE  
SCOPE AND REQUIREMENTS OF THE WORK

FOR

Maintenance Works  
Civil & Maintenance works at Darroobalgie HVIS  
Sth Bound

Compliance Operations Branch

Document No:  
Version: 1.0  
Issue Date: 26 Feb 2018

---

**RECORD OF AMENDMENTS**

Version	Summary	Date	Approved
1.0	Initial draft	26 Feb 2018	

## CONTENTS

<b>DEFINITION AND GLOSSARY OF TERMS .....</b>	<b>4</b>
<b>1 INTRODUCTION .....</b>	<b>5</b>
<b>2 STANDARDS AND SPECIFICATIONS.....</b>	<b>5</b>
2.1 AUSTRALIAN STANDARDS.....	5
2.2 RMS SPECIFICATIONS AND DOCUMENTS .....	5
2.3 ISSUES OF STANDARDS, SPECIFICATIONS AND DRAWINGS.....	6
2.4 COMPLIANCE WITH SPECIFICATIONS .....	6
2.5 PRECEDENCE OF SPECIFICATIONS.....	6
<b>3 LOCATIONS .....</b>	<b>7</b>
<b>4 SCOPE OF WORK.....</b>	<b>7</b>
<b>5 PROJECT SCHEDULE .....</b>	<b>9</b>
<b>6 GENERAL WORK MANAGEMENT REQUIREMENTS.....</b>	<b>9</b>
6.1 MANAGEMENT OF THE WORK.....	9
6.2 ACCESS TO SITES.....	10
6.3 INDUSTRIAL RELATIONS MANAGEMENT .....	10
<b>7 STATEMENT OF WORK .....</b>	<b>11</b>
7.1 PROJECT DELIVERABLES.....	11
7.2 PROJECT MANAGEMENT PLAN .....	12
7.3 PROJECT PROGRAM .....	12
7.4 RISK MANAGEMENT PLAN .....	12
7.5 INSTALLATION MANAGEMENT PLAN.....	13
7.6 PROGRESS REPORT REQUIREMENT .....	13
7.7 QUALITY ASSURANCE.....	13
<b>8 WARRANTY.....</b>	<b>13</b>
<b>9 DOCUMENTATION.....</b>	<b>14</b>
<b>10 APPENDIX A.....</b>	<b>16</b>

## DEFINITION AND GLOSSARY OF TERMS

The following definitions and abbreviations shall apply to this Specification.

AS	Australian Standard
Authority, or the Authority	The Roads and Maritime Services of New South Wales
DMP	Design Management Plan
IEC	International Electro technical Commission
ISO	International Organization for Standardization
NZS	New Zealand Standard
OEM	Operational Engineering Maintenance
OH&S	Occupational Health and Safety
PMP	Project Management Plan
RFQ	Request for Quotation
RFT	Request for Tender
RMP	Risk Management Plan
RMS	Roads and Maritime Services, NSW
ROL	Road Occupancy Licences
TMC	Traffic Management Centre
WAE	Work As Executed
RMS representative	RMS Project Manager

## 1 INTRODUCTION

The intent of this document is to provide the Service Provider with a summary of what this project requires to tender for the job.

The HVIS site at Daroobalgie carried out enforcement operations intercepting Heavy Vehicles on the Newell Highway. There currently exists two sites, north and south bound. Both sites are currently manned by two inspectors each approximately 16 hours a day, split between two hour shifts.

RMS is seeking to facilitate an amenities building to one HVIS site at the current moment, it is envisaged that this amenities building is used exclusively by the Heavy Vehicles inspectors on site and not by the public.

Water connections are believed to be present on site, however an onsite inspection can verify the exact amount of excavation required from the connection point to the location of the amenities building.

The exact location of the amenities building will be decided on site by the RMS PM, an indicative location is shown within the attached schematic diagrams.

The type of system to be installed is also specified within the attached specifications, the REF is being completed by RMS and the approval is based on the type of system specified within this RFT.

## STANDARDS AND SPECIFICATIONS

### 1.1 Australian Standards

All work shall comply with the following standards.

AS/NZS 3000	Electrical installations (known as the Australian/New Zealand Wiring Rules)
AS/NZS 1768:2007	Lightning Protection Including Risk assessment
AS/NZS ISO 9001	Quality management system - Requirements
AS/NZS 4360	Risk Management
AS/NZS ISO 14000	Environmental Management Standards
AS/NZS 4801	Occupational Health & Safety Management System

### 1.2 RMS Specifications and Documents

All work shall comply with the following RMS Specifications and Documents.

This document shall be used in conjunction with the referencing documents. The following documents are referenced in this specification and shall be considered to form part of this specification:

#### Document Title

AS-1074: Steel Tubes And Tubular For Ordinary Service

AS-1289: Methods of Testing Soils for Engineering Purposes  
 AS-1165: Acoustics - Rating of sound absorption - Materials and systems  
 AS-2053: Conduits and Fittings for Electrical Installations  
 AS-3000: Electrical installations-buildings, structures and premises (known as the SAA Wiring Rules) Specification  
 AS-3080: Telecommunications Installations – Integrated telecommunications cabling systems for commercial premises  
 AS-3084: Telecommunications Installations – Telecommunications pathways and spaces for commercial buildings  
 AS-3085: Telecommunications Installations – Administration of communications cabling systems – Basic requirements  
 AS-3600: Concrete Structures  
 AS-3996: Metal Access Covers, Road Grates and Frames  
 RMS3051: Specification for the Supply and Delivery of Base and Sub-Base Materials for Surfaced Roads Pavements  
 RMS R41: Clearing  
 RMS R57: Design of Reinforced Soil Walls  
 RMS G10: Control of Traffic  
 RMS G21/G22 RMS's Occupational Health & Safety (OH&S)  
 RMS G35/G36 Guide to QA Specifications – Environmental Protection  
 RMS PCF2 Equipment Specification – Pit covers and frames

### **1.3 Issues of Standards, Specifications and Drawings**

All Standards, Specifications and Drawings shall be the versions that are current seven (7) days prior to the close of quotations, including errata, amendments and addenda that may be issued from time to time.

It shall be the responsibility of the Service Provider to obtain the relevant versions of such documents, specifications and drawings referred to in this Specification from the relevant issuing bodies.

### **1.4 Compliance with Specifications**

All equipments and materials, where not specified otherwise, shall be in accordance with Australian/New Zealand Standard Specifications, where such exist, and in their absence, with appropriate IEC or ISO Specifications.

Electrical installation works shall comply with the safety requirements of the National Electrical Codes AS/NZS 3000 and AS/NZS 3100.

All installation and commissioning works shall comply with the requirements of the NSW Occupational Health and Safety Act.

### **1.5 Precedence of Specifications**

In the event of any conflict between the referenced specifications, the order of precedence shall be as follows:

- this Scope and Statement of Work document;
- Australian Standards; and
- IEC and ISO Specifications

## 2 LOCATIONS

Refer to Appendix A for diagram

## 3 SCOPE OF WORK

Roads and Maritime is requesting the submission of a lump sum fee estimate for the installation of Amenities block on the Sth bound site, concrete pad on the sth side approach to the weighbridge at Daroobalgie HVIS on the Newell High way.

The works involve the following:

- Transportation of Amenities to site
- Provision of utility surveys
- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.
- Installation of Septic pump tanks as per attached designs and specifications at Daroobalgie Nth bound site. Septic to be a 5L system, RMS to provide specification.
- Installation of amenities block Sth bound, exact location shown in images within appendix, block also shown on attached design.
- Excavation for council water supply
- Dumping of unwanted materials
- Connection of water supply by a licenced plumber.
- Excavation and dumping of 15 meters of flexible pavement to a depth of 350mm and allowance for dumping costs at both Daroobalgie Nth and Sth.
- Formwork, provision of steel and concreting 13m long by 6 m wide to a depth of 250mm, cross section drawing to be provided at both Daroobalgie Nth and Sth.
- Line marking of areas around the newly installed concrete pad in addition to the installation a 5mx5m stop sign at both Nth and Sth bound sites prior to the weighbridge.( Current stop marker is faded)
- Installation of two stop signs with posts
- Cleaning of the area and make good.

Site information and scope will be further provided below.

The scope of the works also includes the below items but is not limited to:

- Management of the work including project management, coordination with RMS PM and other stakeholders according to the requirements of this document;
- Management of OH&S strategies and plans for the entire project including submitting Traffic Management Plans used at the Sites where safety to workers and the public is at risk and where potential disruptions to traffic are likely to occur, as required by RMS;
- Works carried out shall be based on the site-specific inspection as well as General Site Layout Drawings if required, consultation with and approval from RMS's representative is required prior to any works commencing.
- The contractor shall prepare and submit plans for RMS to review and approve prior to implementation if RMS's representative deems necessary for that particular body of works.

- The contractor shall prepare and submit construction plans for review and approve prior to implementation;
- The contractor shall co-ordinate and manage the use of lifting machinery, any other equipment, and any site related activities with accordance to Australian OH&S Requirements & Australian Standards;
- The contractor will organise searches for underground utility services report, and obtain Geotechnical report if required;
- RMS representative will liaise with Environmental Services Branch to prepare the Minor Works REF (Review of Environmental Services) if required;
- RMS representative will liaise with Infrastructure Communications to consult and develop / issue notifications to local residences.
- The contractor will organise and obtain agreement with relevant utility companies for underground / aboveground work relocation works;
- The contractor will provision all site coordination works, all required equipment and materials and compliance with relevant requirements from the local council and other authorities when and as required for all sites;
- Submission of application for Service Mark;
- Trenching, Conducting and Cabling for Power (Orange) and Comms (White), as per Construction of Underground Cableways Specification
- Provision of Site Acceptance Tests with the witness of RMS staff if required;
- Provision of Commissioning Test with the witness of RMS staff if required;
- Provision of As-Built drawings and O&M Documents if required;
- Submit regular weekly progress reports according to the requirements of the Statement of the Work document;
- The contractor shall attend, along with other stakeholders ( as required) , Monthly Project Review meetings; and discuss/resolve site issues ( as part of table provided) , any drawings, equipment, installation and test issues, defects or any other issue relating to the project and list of works;
- The contractor will endeavour to minimise the number of NCR(s) identified during Final Inspection. If NCR(s) are identified, NCR(s) are to be resolved within 30 business days.
- Once all NCR have been resolved for a site, The contractor is to provide RMS all handover documentation including as built drawings, photos, SWMS documentation, risk reports, as per within 30 business days.

**ANY Additional works requested by RMS for the above to be considered as a variation**



## 4 PROJECT SCHEDULE

The program milestone is as shown below:

	Deliverables	Due Date
1	Award Tender	2 March 2018
2	Risk Management Workshop	
4	Utility checks and relocation if required	
5	As-built drawings and O&M documents	
6	Handover to RMS	
7	Project completion	
8		
9		
10		
11		
12		
13		
14		
15		
16		
17		
18		

Table 2: Project deliverables

## 5 GENERAL WORK MANAGEMENT REQUIREMENTS

### 5.1 Management of the Work

The Service Provider shall have a management system in place for the purpose of removal of site work supervision and management, coordination, and monitoring of all work under this RFQ.

The project manager shall be a suitably qualified person with the following minimum qualifications:

- 
- a) Good working knowledge of OH&S Regulations;
  - b) Extensive experience in facilitating and ensuring safe working on public roadways;
  - c) Demonstrable ability to lead a team of multi-discipline staff; and
  - d) Extensive experience in managing the maintenance works and installation of roadside devices projects.
  - e) The Service Provider's personnel who are going to undertake works such as traffic control, or operating elevated work platforms, lifting cranes, back-hoes, boring machines or other machinery, shall have the relevant accreditation training and be in possession of an appropriate current and valid licence for the work.

## **5.2 Access to Sites**

- a) Where necessary, possession of the Site must be coordinated with RMS. Road Occupancy Licences (ROL) must be obtained from the TMC prior to commencement of work if work undertaken will impact on traffic conditions and road safety. The TMC will require a minimum of 15 days notification on any ROL.
- b) The Service Provider must notify RMS representative if they cause damage to the Site or are being prevented from accessing the Site.
- c) The Service Provider must follow safe working practices to ensure the safety of the public and workers as per NSW Government & the RMS OH&S guidelines and requirements. The Service Provider must submit a Safe Work Method Statement prior to commencing work.
- d) The Service Provider must follow environmental working practices as per RMS and EPA guidelines and requirements.
- e) The Service Provider must conduct risk assessments of the Site and report any unsafe matters associated with the installation, testing, commissioning and/or removal of equipment and mounting structures.

## **5.3 Industrial Relations Management**

The Service Provider shall comply with the NSW Government Industrial Relations Management Guidelines and requirements.

The industrial relations management requirements in this Quotation may be in addition to, but are not in substitution for, any other requirement of legislation or regulations and do not limit the powers of the RMS's Representative or the liabilities and responsibilities.

- a) Before starting work on the site, in accordance with the NSW Government Industrial Relations Management Guidelines, the Service Provider shall prepare and submit:
- b) Evidence of compliance with all employment and legal obligations in the previous twelve months;

- 
- c) The location of time and wage records and other documents that are required to be kept to verify ongoing compliance with all employment and legal obligations;
  - d) The names of Federal or NSW awards that are likely to cover subcontractors and other contractors on the project;
  - e) The names of those responsible for coordinating industrial relations on the project; and outline of:
    - Consultation and communications mechanisms;
    - Measures to coordinate the interface with subcontractors, other contractors and unions;
    - Measures for assessing subcontractors; and
    - Measures to monitor and verify ongoing compliance.

## 6 STATEMENT OF WORK

### 6.1 Project Deliverables

The project management methodologies that shall be utilised by the Service Provider for this project shall be in line with the nominated standards and shall be clearly explained in the Project Management Plan.

As a minimum the following are the required deliverables and/or outcomes for this project.

- a) Project Management Plan (PMP) (see below) if and when required ( pending of works being carried out, RMS to advise)
- b) Project Program (see below)
- c) Risk Management Plan, risk register and risk assessment report for the project (see below). This can form an independent section of the PMP
- d) Installation Management Plan (see below) if required
- e) Quality Management Plan
- f) OH&S Plan
- g) Environmental Management Plan if required
- h) Site Management Plan if required
- i) Work-As-Executed drawings
- j) Regular Fortnightly Progress Report (see below)

---

## 6.2 Project Management Plan

The Project Management Plan shall address and include the following project related issues:

- a) Project schedule, project change management, project risks management, and procurement management.
- b) Include project organisation and responsibilities and communication process and protocol between different stakeholders including RMS and any external stakeholders,
- c) Include details of the removal activities, deliverables, documentation and reviews ,
- d) Include details of the installation activities, deliverables, documentation and reviews ,
- e) Identify the interdependencies between the deliverables and milestones,
- f) Include all activities to be undertaken,

## 6.3 Project Program

The Project Program shall:

- a) Include resource requirements and resource allocations, including the identification of people and responsibilities;
- b) Identify the interdependencies between the stages, deliverables and milestones, and activities;
- c) Include all activities to be undertaken.

## 6.4 Risk Management Plan

The strategy and approach for delivering project as a whole and the different stages of the project shall be integrated with risk assessment and management processes.

The risk assessment and management processes and procedures shall be based on AS/NZS 4360:1999.

The RMP shall be supported by a risk register that is updated throughout the Project term. The following issues must be dealt with in this process.

- a) Assess the risks of the timing of the deliverables and processes; and
- b) Provide specific treatment and mitigation action plans to address high or significant development and integration risks.

---

## 6.5 Installation Management Plan

The Service Provider shall deliver the documentation listed in this document or decided in the early stage of the project to the satisfaction of RMS representative in a timely manner.

## 6.6 Progress Report Requirement

Reports provided by the Service Provider to RMS shall consist of:

- a) The updated Project Program to reflect the latest status of the project, milestones, deliverables and resources.
- b) All changes to the scope since the last period, which may impact the Project Program;
- c) The current version of the risk register, which shall be up-to-date;
- d) Details of actual progress compared with the planned time and resource estimates in quantifiable amounts (not perceived percentages);

## 6.7 Quality Assurance

The Service Provider and its subcontractors (if any) shall follow the ISO9001 Quality Assurance standards in performing the work activities.

The Service Provider shall conduct periodic audits to ensure quality assurance and safety standards are being followed by its personnel and subcontractors personnel.

RMS will conduct quality audit of the Service Provider's and subcontractors' quality system for the works. This requires the cooperation of the Service Provider and support of the audit by providing the necessary records and documentation when requested by RMS.

The Service Provider shall rectify all the non conformance cases within the agreed timeframe and submit a report on the remedial actions that have been taken.

## 7 WARRANTY

The Service Provider shall provide a warranty against poor workmanship, work defects, equipment defects and any other causes of malfunctions for a period of 1 year commencing from the date of acceptance by and handover to RMS. The Service Provider shall bear all costs to rectify the above during the warranty period.

---

## 8 DOCUMENTATION

The Service Provider shall provide all necessary documentation for the project, including:

- Project Management and other related plans;
- Work-As-Executed Drawings; and



---

## 9 APPENDIX A

The following Annexure and Schedules form part of this quote:





## Nuix-defined

## Metadata

File Size	451947
File Type	application/pdf
GUID	8b099277-4d3f-4ba2-8729-10520597a2f5
Item Date	2018-02-26T14:46:27.850+11:00
MD5 Digest	4e25e4afbe5a798569b1ee23b85f504
Path Name	/E18-0736-AS-7-1-PR-0004/E18-0736-AS-7-1-PR-0004.E01/[Unnamed Disk Image]/Local Disk/[File System Root]/Users/duboisA/Desktop/to be transfered/Daroolgabie HVIS/Amenities Installation RFQ Sth bound
Shannon Entropy	7.984882624078964

## User-defined

## Evidence Metadata

Property Source	E18-0736-AS-7-1-PR-0004
Properties	
Application Created	2018-02-26T14:46:27.000Z
Application Modified	2018-02-26T14:46:27.000Z
Author	DuboisA
Compressed	false
File Accessed	2018-02-26T03:46:41.313Z
File Changed	2018-02-26T03:46:27.850Z
File Created	2018-02-26T03:46:41.270Z
File Group	Domain Users (S-1-5-21-1629583213-1224749553-1844936127-513)
File Group SID	S-1-5-21-1629583213-1224749553-1844936127-513
File Modified	2018-02-26T03:46:27.850Z
File Offset	80696811520
File Owner	S-1-5-21-1629583213-1224749553-1844936127-63909
File Owner SID	S-1-5-21-1629583213-1224749553-1844936127-63909
File Start Cluster	19701370
File Start Sector	157610960
Name	RFQ Scope of Work Amenities 26022018.pdf
NTFS ACE 1 Access Mask	{Read,Write,Write,Read Extended Attributes,Write Extended Attributes,Execute File,Delete Child,Read Attributes,Write Attributes,Delete,Read Security Descriptor,Write DACL,Write Owner,Synchronize}
NTFS ACE 1 Flags	Unknown Flags: 0x10
NTFS ACE 1 Raw Access Mask	2032127
NTFS ACE 1 Raw Flags	16

NTFS ACE 1 SID S-1-5-18  
 NTFS ACE 1 SID Name Local System  
 NTFS ACE 1 Type Allow  
 NTFS ACE 2 Access Mask {Read,Write,Write,Read Extended Attributes,Write Extended Attributes,Execute File,Delete Child,Read Attributes,Write Attributes,Delete,Read Security Descriptor,Write DACL,Write Owner,Synchronize}  
 NTFS ACE 2 Flags Unknown Flags: 0x10  
 NTFS ACE 2 Raw Access Mask 2032127  
 NTFS ACE 2 Raw Flags 16  
 NTFS ACE 2 SID S-1-5-32-544  
 NTFS ACE 2 SID Name BUILTIN\Administrators  
 NTFS ACE 2 Type Allow  
 NTFS ACE 3 Access Mask {Read,Write,Write,Read Extended Attributes,Write Extended Attributes,Execute File,Delete Child,Read Attributes,Write Attributes,Delete,Read Security Descriptor,Write DACL,Write Owner,Synchronize}  
 NTFS ACE 3 Flags Unknown Flags: 0x10  
 NTFS ACE 3 Raw Access Mask 2032127  
 NTFS ACE 3 Raw Flags 16  
 NTFS ACE 3 SID S-1-5-21-1629583213-1224749553-1844936127-63909  
 NTFS ACE 3 SID Name S-1-5-21-1629583213-1224749553-1844936127-63909  
 NTFS ACE 3 Type Allow  
 NTFS ACE 4 Access Mask {Read,Write,Write,Read Extended Attributes,Write Extended Attributes,Execute File,Delete Child,Read Attributes,Write Attributes,Delete,Read Security Descriptor,Write DACL,Write Owner,Synchronize}  
 NTFS ACE 4 Flags Unknown Flags: 0x10  
 NTFS ACE 4 Raw Access Mask 2032127  
 NTFS ACE 4 Raw Flags 16  
 NTFS ACE 4 SID S-1-5-21-1629583213-1224749553-1844936127-12471  
 NTFS ACE 4 SID Name S-1-5-21-1629583213-1224749553-1844936127-12471  
 NTFS ACE 4 Type Allow  
 NTFS Attributes Archive

NTFS File Name  
 Attribute DOS File 2018-02-26T03:46:41.313Z  
 Accessed  
 NTFS File Name  
 Attribute DOS File 2018-02-26T03:46:41.313Z  
 Changed  
 NTFS File Name  
 Attribute DOS File 2018-02-26T03:46:41.270Z  
 Created  
 NTFS File Name  
 Attribute DOS File 2018-02-26T03:46:41.313Z  
 Modified  
 NTFS File Name  
 Attribute DOS File RFQSCO~1.PDF  
 Name  
 NTFS File Name  
 Attribute Win32 2018-02-26T03:46:41.313Z  
 File Accessed  
 NTFS File Name  
 Attribute Win32 2018-02-26T03:46:41.313Z  
 File Changed  
 NTFS File Name  
 Attribute Win32 2018-02-26T03:46:41.270Z  
 File Created  
 NTFS File Name  
 Attribute Win32 2018-02-26T03:46:41.313Z  
 File Modified  
 NTFS File Name  
 Attribute Win32 RFQ Scope of Work Amenities 26022018.pdf  
 File Name  
 NTFS Hard Links 2  
 NTFS LogFile  
 Sequence Number 33258150676  
 NTFS MFT Index 177371  
 NTFS MFT  
 Resident false  
 NTFS Parent MFT  
 Index 194546  
 Page Count 17  
 PDF Certification  
 Level Not Certified  
 PDF Contains  
 Annotations false  
 PDF Contains  
 Comments false  
 PDF Creator PScript5.dll Version 5.2.2

PDF Encryption Level	None
PDF Images JPEG	2
PDF Javascript Present	false
PDF Metadata Encrypted	false
PDF Portfolio	false
PDF Producer	GPL Ghostscript 8.15
PDF Version	4
Physical Start Sector	158622672
Title	Microsoft Word - RFQ Scope of Work Amenities 26022018.doc

## Daroobalgie Sth Amenities and VSLS signs

---

**From:** DUBOIS Alexandre </o=rta/ou=exchange administrative group (fydibohf23spdl)/cn=recipients/cn=alexandu">  
**To:** DUBOIS Alexandre <alex.p.dubois@rms.nsw.gov.au>  
**Bcc:** Cbf Project [REDACTED] o@[REDACTED], info@[REDACTED], oz corp civil <admin@[REDACTED]>  
**Date:** Mon, 26 Feb 2018 14:47:32 +1100  
**Attachments:** 3550L Septic Tank with 10,000L Collection Well.pdf (263.22 kB); NSW Accreditation - Septic Tanks and Collection Wells.pdf (2.98 MB)

---

Good afternoon,

RMS is seeking the quotation for the installation of Amenities block at Daroobalgie, RFQ attached

Can you please provide the quotation by COB 2<sup>nd</sup> of March.

Thank you

Regards,

**Alex Dubois**


Project Manager

Compliance System [REDACTED] Compliance Operations Branch | Compliance and Regulatory Services


T 02 88370636 | M [REDACTED] 6 298


[www.rms.nsw.gov.au](http://www.rms.nsw.gov.au)


Roads and Maritime Services  
 99 Phillip st Parramatta NSW 2150

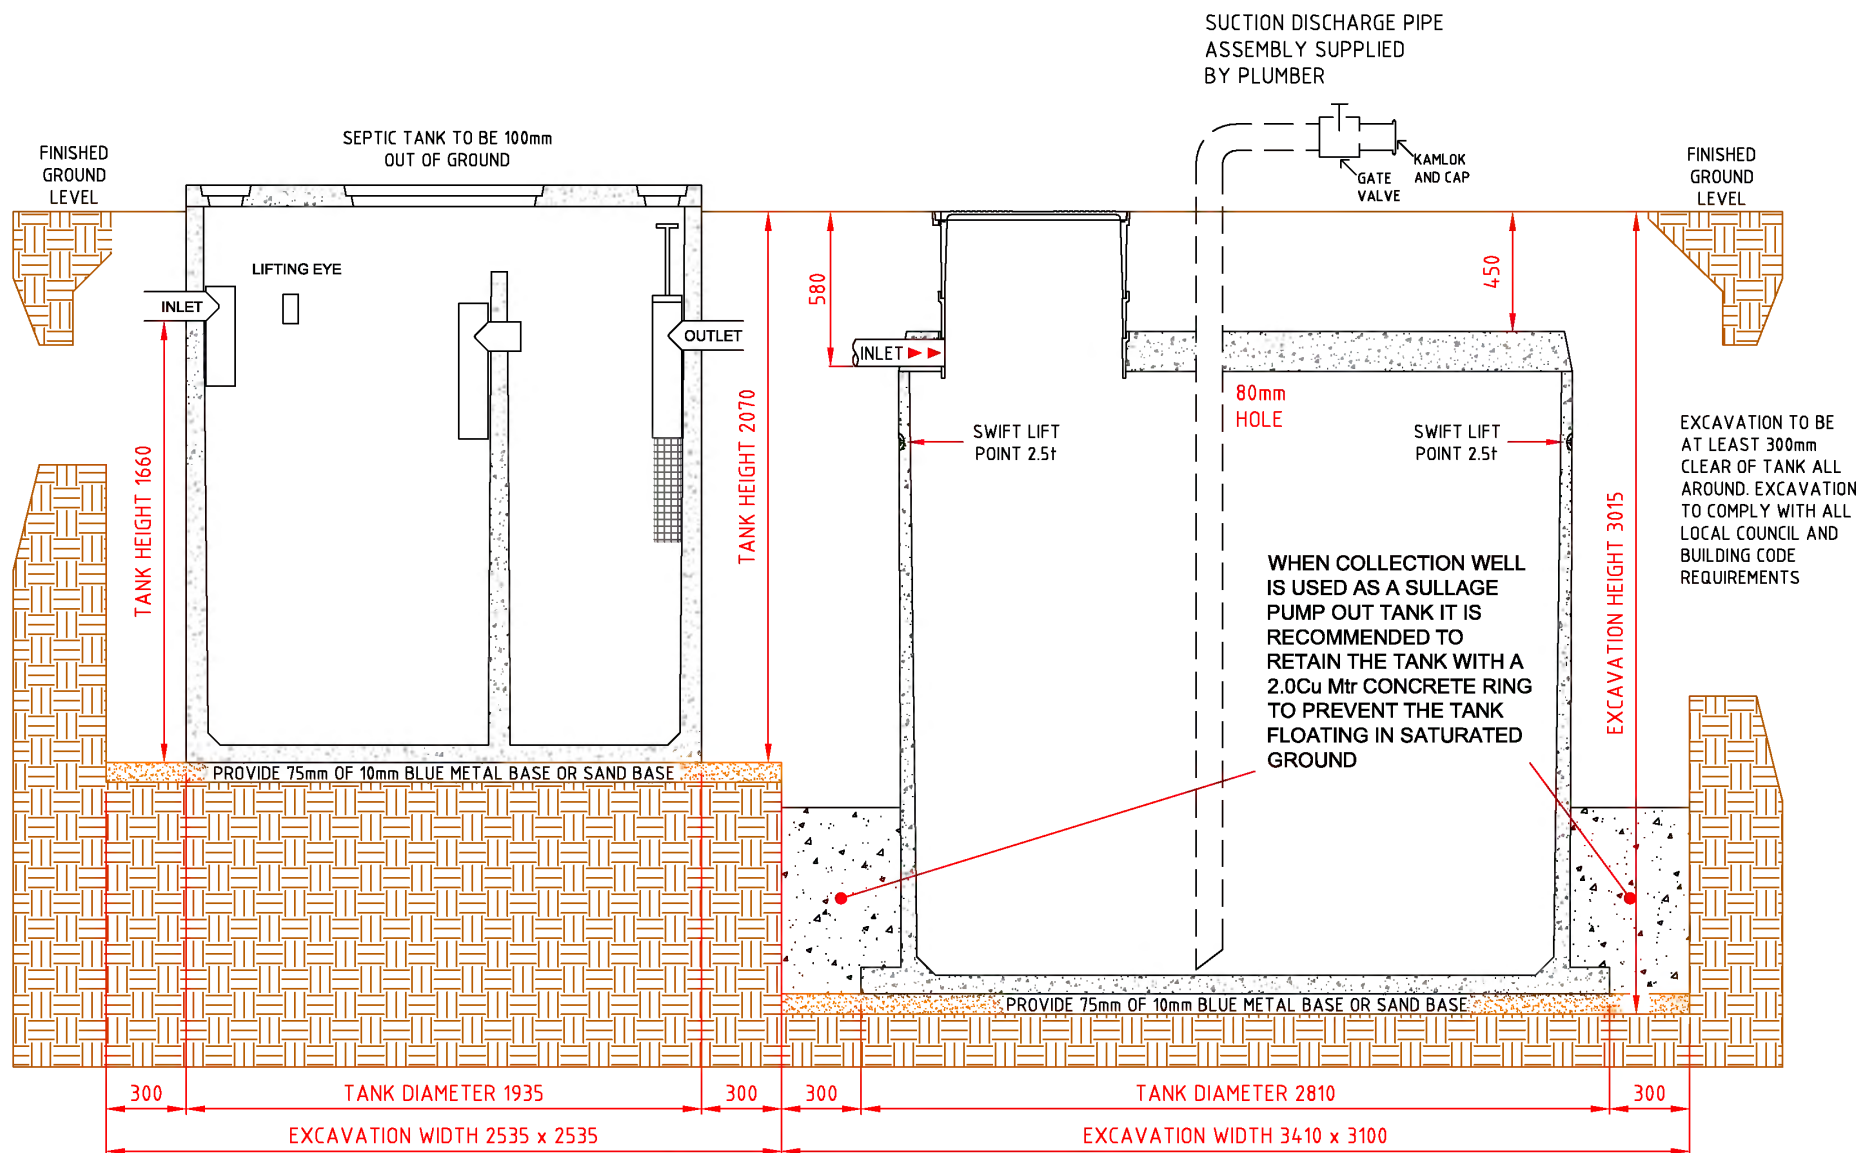

DIAGRAMMATIC SECTION DETAIL

ISSUE	DATE	AMENDMENTS	PROPOSED LAYOUT FOR BIOSEPTIC PUMP OUT SYSTEM 3550L SEPTIC TANK & 10,000L COLLECTION WELL	DRAWN	O.Rios	APPROVED BY	DATE:	<b>BioSeptic Pty Ltd</b> 1 - 5 Anzac Rd, Smeaton Grange Rd Smeaton Grange, NSW 2567 Phone: (02) 4629 6666 Fax: (02) 4629 6655 Email: sales@bioseptic.com.au	 SEWAGE SYSTEMS
A	23.02.16	ORIGINAL ISSUE		APPROVED					
				ISSUED	23.02.16	NAME:			
				RECORD OF ISSUE					
				A					
THESE DRAWINGS & DESIGNS ARE THE PROPERTY OF BIOSEPTIC PTY LTD AND MUST NOT BE COPIED OR USED WITHOUT BIOSEPTIC'S WRITTEN PERMISSION.				SHEET 1 OF 1		SIGNATURE			

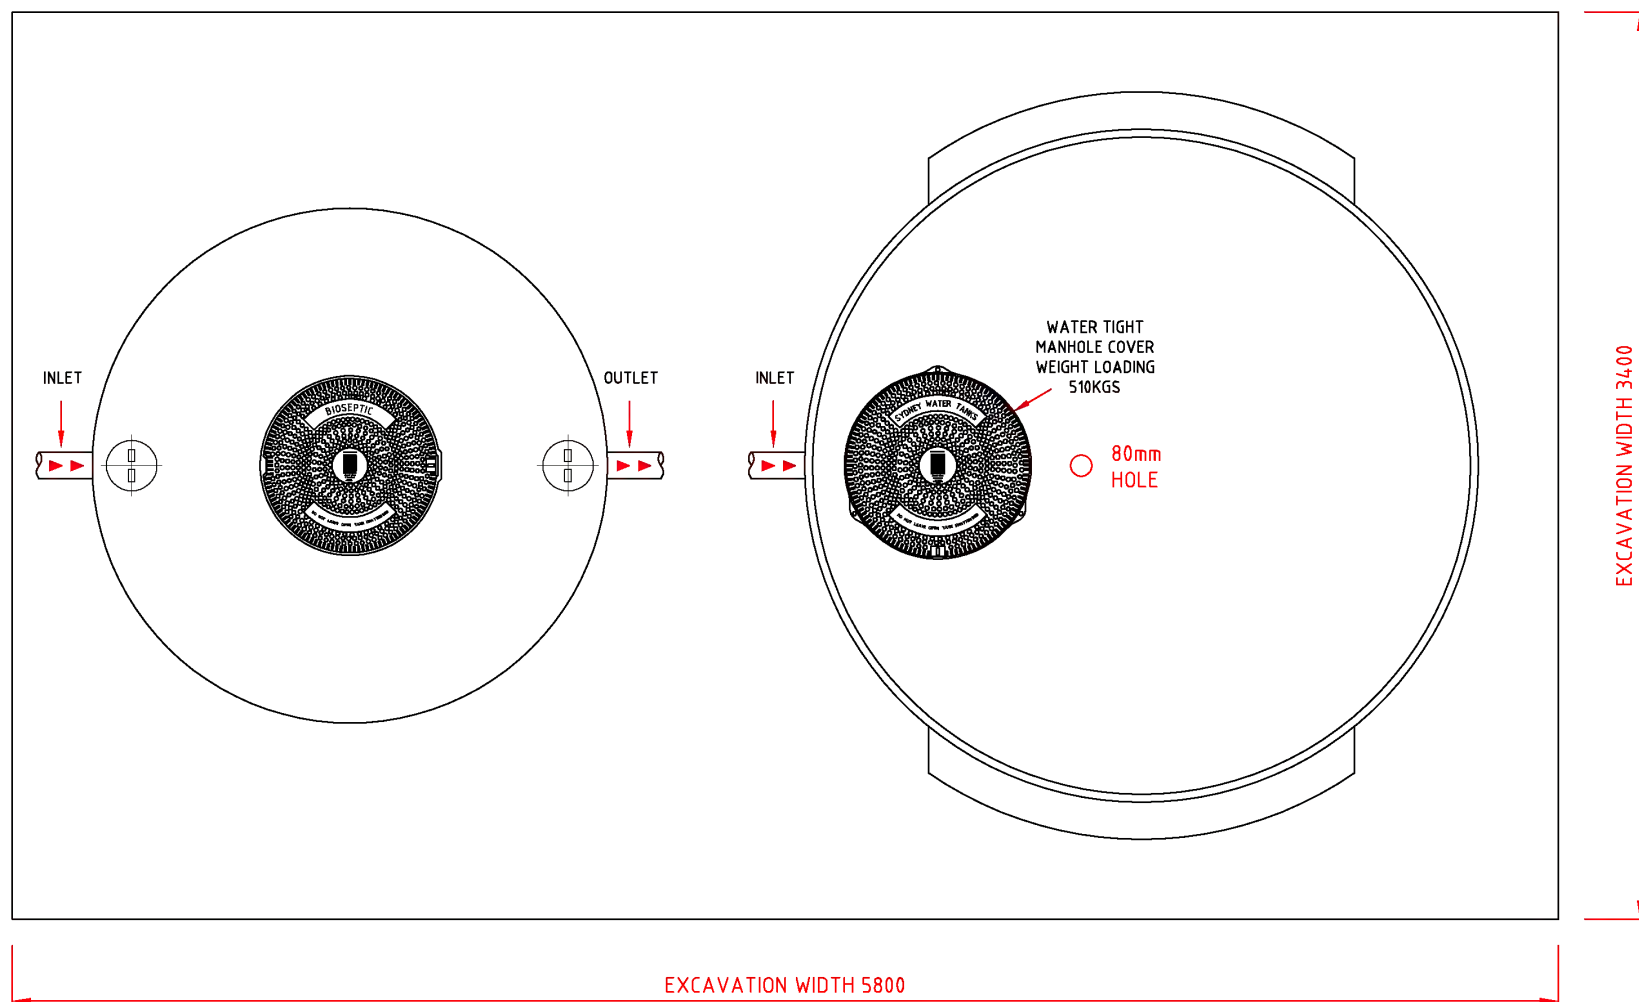

ISSUE	DATE	AMENDMENTS	PROPOSED LAYOUT FOR BIOSEPTIC PUMP OUT SYSTEM 3550L SEPTIC TANK & 10,000L COLLECTION WELL	DRAWN	O.Rios	APPROVED BY	DATE:	<b>BioSeptic Pty Ltd</b> 1 - 5 Anzac Rd, Smeaton Grange Rd Smeaton Grange, NSW 2567 Phone: (02) 4629 6666 Fax: (02) 4629 6655 Email: sales@bioseptic.com.au	 SEWAGE SYSTEMS
A	23.02.16	ORIGINAL ISSUE		APPROVED		NAME:			
				ISSUED	23.02.16				
				RECORD OF ISSUE					
				A					
THESE DRAWINGS & DESIGNS ARE THE PROPERTY OF BIOSEPTIC PTY LTD AND MUST NOT BE COPIED OR USED WITHOUT BIOSEPTIC'S WRITTEN PERMISSION.				SHEET 1 OF 1		SIGNATURE			





# Certificate of Accreditation

## Septic Tanks & Collection Wells

*This Certificate of Accreditation is hereby issued by the Director-General of the NSW Ministry of Health pursuant to Clause 41(1) of the Local Government (General) Regulation 2005.*

*Manufacturer:*        **BioSeptic Pty Ltd**

*Of:*                      **1-5 Anzac Avenue, Smeaton Grange, Narellan, NSW, 2567**

*This is to certify that the septic tanks and collection wells, as described in the attached Schedule, have been accredited as a sewage management facility for use in single domestic premises in NSW. The septic tanks and collection wells are manufactured to the Australian/New Zealand Standard AS/NZS 1546.1:2008 – On-site domestic wastewater treatment units – Septic Tanks.*

A handwritten signature in black ink, appearing to be 'D. L. L.' or similar, located below the certification text.

*A/Director, Environmental Health Branch  
for Director-General (delegation PH335)*

*Date of Issue: 11 September 2013*

*Certificate No: 003-21556*

**This Certificate of Accreditation is in force until 31 December 2018**



Health

# Accreditation Schedule

*The Certificate of Accreditation applies to the following  
septic tanks and collection wells.*

Model	Description	Size
Septic Tank	Vertical axis type, cylindrical precast steel fibre reinforced concrete, with lid, access cover, inlet and outlet fittings.	3550 L
Collection Well	Vertical axis type, cylindrical precast steel fibre reinforced concrete, with lid, access cover and inlet fitting.  Certification applies only to the construction of the tank, lid and access cover. It does not include internal fittings or partitions.	3750 L 7200 L  3800 L 5000 L 6100 L 10,000 L
Pump Well	Vertical axis type, cylindrical precast steel fibre reinforced concrete.	1100L
Combined Septic tank/ Collection well	Vertical axis type, cylindrical precast steel fibre reinforced concrete, with lid, access cover and inlet fitting.  Certification applies only to the construction of the tank, lid and access cover. It does not include internal fittings or partitions.	2300 L/4700 L 2750 L/5500 L  2300 L/6000 L

*Date of Issue: 11 September 2013*


*Certificate No: 003-21556*

**This Certificate of Accreditation is in force until 31 December 2018**



# 3550L SEPTIC TANK

## SPECIFICATIONS

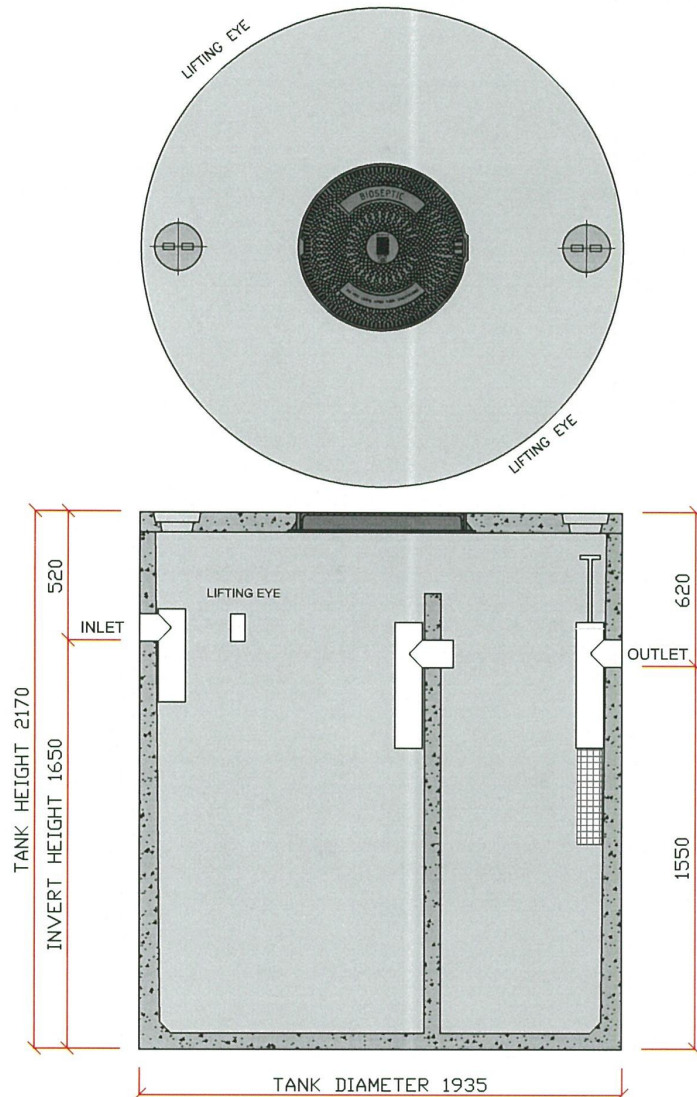

**2000L**  
Per Day  
Capacity

**x13**  
on town  
water supply

PRODUCT GUIDE

Septic Tank Capacity	3550L
Primary Chamber Capacity	2367L
Secondary Chamber Capacity	1183L
Stainless Steel Outlet Filter	Yes
Lid Load Limit	510kg
Tank Weight	3600kg
NSW Health Accredited	003-21556



AS1546.1  
Lic SMK21556

### DESCRIPTION

### FEATURE

### BENEFIT

3550 Litre Baffled Septic Tank	30 Years Warranty on Concrete Components	Long Warranty Period Provides Peace of Mind
Australian Manufactured & Accredited to AS/NZS 1546.1:2008 - Septic Tanks	Wet Cast 40mpa Fibre Steel Reinforced Concrete Construction with <b>Integrated</b> Baffle	Concrete is the Traditional Material for Septic Tanks & Has Been Proven to Last
Quality Assured by SAI Global, Lic. No SMK21556	Supplied with Stainless Steel Outlet Filter and Two Outlet Squares	Prevents the Carry Over of Sludge & Suspended Solids to the Trench or ETA Bed to extend its Life
NSW Health Certification of Accreditation 003-21556	New Generation <b>Lockable</b> Composite Resin Access Covers	Prevents Access by Children. Stronger than Steel of the Same Weight
BioSeptic has it's OWN Service Division for After Sales Service	Access Cover Weighs only 8.5kgs	Easy to Lift. Provides good WHS compliance
Suitable for Domestic & Small Commercial Applications	510kgs Access Cover Loading	Suitable for Pedestrian Traffic Only

1300 658 111 | Fax: (02) 296 655 | [sales@bioseptic.com.au](mailto:sales@bioseptic.com.au) | [www.bioseptic.com.au](http://www.bioseptic.com.au)  
1-5 Anzac Avenue, Smeaton Grange, NSW, 2567 | PO Box 3250, Narellan, NSW, 2567  
BioSeptic Pty Ltd ABN 95 056 461 226

**M** THE MARTINS GROUP

Sydney **WaterTanks**  
superior engineering

SWT **Onsite Detention Tanks**



SWT Concrete **Pits & Grates**

**BIO**  
**septic**  
SEWAGE SYSTEMS



# 1100L PUMP STATION

## SPECIFICATIONS

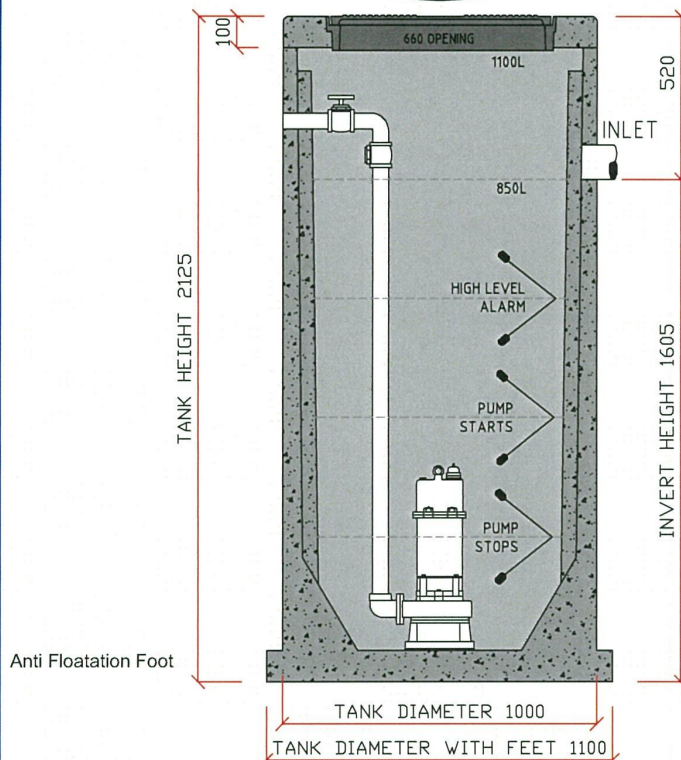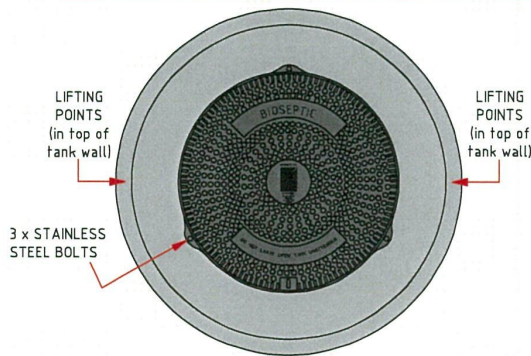

**1100L**  
Tank  
Capacity

**Grinder  
Pump &  
High Water  
Alarm**

Total Capacity	1100L
Capacity Below Inlet	850L
High Level Alarm Operates	435L
Pump Starts	335L
Pump Cycle	200L
Tank Weight	1500kg
NSW Health Accredited	SEPS 016



AS1546.1  
Lic SMK21556

WHEN BACKFILL IS SUITABLY  
PLACED AND COMPACTED IN  
ACCORDANCE WITH AS 3798-2007  
THE PUMP STATION WILL HAVE A  
RESISTANCE TO FLOATING OF 3 KN.

### DESCRIPTION

### FEATURE

### BENEFIT

1100 Litre Sewage Ejection Pump Station	30 Years Warranty on Concrete Components	Long Warranty Period Provides Peace of Mind
Australian Manufactured & Accredited to AS/NZS 1546.1:2008 - Septic Tanks	Wet Cast 40mpa Fibre Steel Reinforced Concrete Construction	Concrete is the Traditional Material for Septic Tanks & has been Proven to Last
Quality Assured by SAI Global, Lic. No SMK21556	New Generation <b>Lockable</b> & Sealed Composite Resin Access Cover, Weighing only 9 Kgs	Prevents Access by Children. Stronger than Steel of the Same Weight
NSW Health Certification of Accreditation 003-21556	510kgs Access Cover Loading Access Cover has 660mm Clear Opening	Easy to Lift. Provides good WHS compliance
BioSeptic has it's OWN Service Division for After Sales Service	Centrifugal Grinder Pump. Non Return and Gate Shut Off Valve	
Suitable for Domestic & Small Commercial Applications	High Water Audio/Visual Alarm with Mute Facility Mute Facility Resets after 2 Hours	

1300 658 111 | Fax: (02) 296 655 | sales@bioseptic.com.au | www.bioseptic.com.au  
1-5 Anzac Avenue, Smeaton Grange, NSW, 2567 | PO Box 3250, Narellan, NSW, 2567  
BioSeptic Pty Ltd ABN 95 056 461 226

**M** THE MARTINS GROUP

Sydney  
**WaterTanks**  
superior engineering

SWT  
Onsite Detention  
Tanks

SWT Concrete  
**Pits & Grates**

**Bio  
septic**  
SEWAGE SYSTEMS

*Quality is Our Goal*



Date February 28, 2018

PO #

Quote #	ECMQ00303
---------	-----------

Customer ID	RMS
-------------	-----

**ABN: 26 604 934 698**

## Customer:

## Roads and Maritime Services

Attention: Alexandre Dubois

ABN: 76 236 371 088

110 George St, Parramatta NSW 2150

(02) 8849 2633

### Quote/Project Description

**The works Quote involved the following : Daroobalgie**

- 1- Installation of toilet cubicle/meeting room and civil works
- 2- Installation concrete pads for weighbridge at Darooabalgie Sth

		Line Total
<b>1- Installation of toilet cubicle/meeting room and civil works</b>		
Carry out utility surveys and DBYD		
Hiring of 80 meters of water filled barriers to block entry to site Sth bound		
Hiring of 120 meters of temporary fencing for excavated areas around the toilet / change room and concreting lead up pavement		
Hire truck with Hiab (crane) for transportation of cubicle from Westmead NSW to Daroobalgie HVIS		
Hire 5 tone Excavator with auger and rock breaker		
Auger of piers and trenching of footings for new location of site toilet / change room		
Supply Aggregate concrete for piers and footings		
Supply Galvanized steel chains and install in concreted piers for anchorage of cubicle		
Hiring of crane to install cubicle over new footing and anchored down.		
Supply 1 x 3500L Bio Septic tank		
Supply 1x 1100 L pump station		
Supply pf 10,000L Collection Well		
Excavate 25m trench and hole for installation of septic tank in ground		
Supply 100mm sewerage pipes for installation from cubicle to septic tank & overflow		
Trench and excavate from septic tank 25m for installation of overflow retention pit		
Excavate level & compact blinding pad for solid base of rainwater tank		
Supply 90mm storm water piping and plumb up from cubicle to tank		
Supply and install electric water pump to cubicle		
Excavate 100m trench to depth of 600mm		
Supply 100m of 1 inch copper pipe		
Plumb water pipe from water meter to cubicle		
Supply and install 3.5 kw air-conditioning split system as requested to toilet/meeting room		
Excavate and formwork for footpath		
Supply concrete and finish footpath to enter cubicle		
Supply truck & Dog to remove unwanted materials		
Supply 9 cubic meter skip bin for removal of rubbish		
Travel, labor hire, accommodation, fuel and expenses		
<b>2- Installation concrete pads for weighbridge at Daroobalgie Sth</b>		
Carry out utility surveys and DBYD		
Excavation of 15 meters of flexible pavement to a depth of 350mm at Sth Bound		
Formwork 13m long by 6m wide to Nth & Sth Bound for concrete pads		
Supply re-enforced steel mesh and rio bars times two layers to Sth bound weighbridge sites		
Supply approx 20 cubic meters of aggregate to each Nth& Sth bound concrete pads = total of 40 cubes		
Finish concrete and screed to RMS requirements for weighing		
Engage surveyor to ensure concreting together with weighbridge meet the Cat 1 requirements		
Supply truck & Dog to remove unwanted materials		
Supply sweeper to clean site and prep for line marking		
Line Marking the perimeter of the newly installed concrete to match current weighbridge line marking		
Paint 5x5 meters stop sign at the Sth bound sites prior to weighbridge		
Install 2 x stop signs with post before weighbridge		
Travel, labor hire, accommodation, fuel and expenses		
<b>Special Notes and Instructions</b>		
Once signed, please Fax, mail or e-mail it to the provided address.	Subtotal	\$ 218,750.00
	Discount	
	Sales Tax Rate	% 10.00
	Sales Tax	
	<b>Total inc GST</b>	<b>\$ 240,625.00</b>

Above information is not an invoice and only an estimate of services/goods described above.  
Payment will be collected in prior to provision of services/goods described in this quote.

Please confirm your acceptance of this quote by signing this document

Signature \_\_\_\_\_

Print Name \_\_\_\_\_

Date \_\_\_\_\_

**Thank you for your business!**

Should you have any enquiries concerning this quote, please contact Barry Haden on [REDACTED] 7 738

■ Donaldson St, ■  
Tel: ■ 7 738 Fax: E-mail: info@■

BSB: 112879 Account Number: 6 088

Nuix-defined  
Metadata

File Size 141312  
 File Type application/vnd.ms-excel  
 GUID a907669a-53fc-41be-9c2b-e0e5433a2e1a  
 Item Date 2018-06-04T10:50:11.000+10:00  
 MD5 Digest 3f2fef44ae619afa5576d9dfbe758cc6  
 Path Name /E18-0736-AS-7-9-PR-0032-UsersFolder/E18-0736-AS-7-9-PR-0032-UsersFolder.Lx01/cbfprojectsptyltd/Desktop/invoice folder  
 Shannon Entropy 6.5356099945826465

User-defined  
Evidence  
Metadata

Property Source E18-0736-AS-7-9-PR-0032  
 Properties  
 Application Version 983040  
 AppName Microsoft Macintosh Excel  
 Author Euro Maintenance and Civil  
 CLSID {00020820-0000-0000-C000-000000000046}  
 Company Euro Maintenance and Civil  
 Contains Comments false  
 Copyright © 2013 Spreadsheet123 LTD  
 Created 2009-07-28T19:11:35.000Z  
 DocSecurity 0  
 Excel Freeze Panes false  
 Excel Hidden Columns true  
 Excel Hidden Rows true  
 Excel Hidden Sheets false  
 Excel Hidden Sheets Count 0  
 Excel Hidden Workbook false  
 Excel Pivot Tables false  
 Excel Print Areas true  
 Excel Protected Sheets false

Excel Very Hidden Sheets	false
Excel Very Hidden Sheets Count	0
Excel Workbook BIFF Info	VI=0x10 VN=0x506 Build=28109 Year=1996
Excel Workbook BIFF Version	7
Excel Workbook Write Protected	false
File Accessed	2018-08-10T01:39:18.000Z
File Changed	2018-06-08T01:59:21.000Z
File Created	2018-02-28T02:48:42.000Z
File Modified	2018-06-04T00:50:11.000Z
Hyperlinks Changed	false
Last Author	Microsoft Office User
Last Printed	2017-12-20T05:46:01.901Z
Last Saved	2018-06-04T00:50:11.764Z
Links Dirty	false
Name	ECM Daroobalgie Quote Sth Bound.xls
Original MD5 Digest	3f2fef44ae619afa5576d9dfbe758cc6
Scale Crop	false
Shared Document	false
Title	Price Quote
Version	1.0.1



*Quality is Our Goal*



Date	February 28, 2018
PO #	
Quote #	ECMQ00303
Customer ID	RMS

**ABN: 26 604 934 698**

## Customer:

## Roads and Maritime Services

Attention: Alexandre Dubois

ABN: 76 236 371 088

110 George St. Parramatta NSW 2150

(02) 8849 2633

### Quote/Project Description

**The works Quote involved the following : Daroobalgie**

- 1- Installation of toilet cubicle/meeting room and civil works
- 2- Installation concrete pads for weighbridge at Darooabalgie Sth

		Line Total
<b>1- Installation of toilet cubicle/meeting room and civil works</b>		
Carry out utility surveys and DBYD		
Hiring of 80 meters of water filled barriers to block entry to site Sth bound		
Hiring of 120 meters of temporary fencing for excavated areas around the toilet / change room and concreting lead up pavement		
Hire truck with Hiab (crane) for transportation of cubicle from Westmead NSW to Daroobalgie HVIS		
Hire 5 tone Excavator with auger and rock breaker		
Auger of piers and trenching of footings for new location of site toilet / change room		
Supply Aggregate concrete for piers and footings		
Supply Galvanized steel chains and install in concreted piers for anchorage of cubicle		
Hiring of crane to install cubicle over new footing and anchored down.		
Supply 1 x 3500L Bio Septic tank		
Supply 1x 1100 L pump station		
Supply pf 10,000L Collection Well		
Excavate 25m trench and hole for installation of septic tank in ground		
Supply 100mm sewerage pipes for installation from cubicle to septic tank & overflow		
Trench and excavate from septic tank 25m for installation of overflow retention pit		
Excavate level & compact blinding pad for solid base of rainwater tank		
Supply 90mm storm water piping and plumb up from cubicle to tank		
Supply and install electric water pump to cubicle		
Excavate 100m trench to depth of 600mm		
Supply 100m of 1 inch copper pipe		
Plumb water pipe from water meter to cubicle		
Supply and install 3.5 kw air-conditioning split system as requested to toilet/meeting room		
Excavate and formwork for footpath		
Supply concrete and finish footpath to enter cubicle		
Supply truck & Dog to remove unwanted materials		
Supply 9 cubic meter skip bin for removal of rubbish		
Travel, labor hire, accommodation, fuel and expenses		
<b>2- Installation concrete pads for weighbridge at Daroobalgie Sth</b>		
Carry out utility surveys and DBYD		
Excavation of 15 meters of flexible pavement to a depth of 350mm at Sth Bound		
Formwork 13m long by 6m wide to Nth & Sth Bound for concrete pads		
Supply re-enforced steel mesh and rio bars times two layers to Sth bound weighbridge sites		
Supply approx 20 cubic meters of aggregate to each Nth& Sth bound concrete pads = total of 40 cubes		
Finish concrete and screed to RMS requirements for weighing		
Engage surveyor to ensure concreting together with weighbridge meet the Cat 1 requirements		
Supply truck & Dog to remove unwanted materials		
Supply sweeper to clean site and prep for line marking		
Line Marking the perimeter of the newly installed concrete to match current weighbridge line marking		
Paint 5x5 meters stop sign at the Sth bound sites prior to weighbridge		
Install 2 x stop signs with post before weighbridge		
Travel, labor hire, accommodation, fuel and expenses		
<b>Special Notes and Instructions</b>		
Once signed, please Fax, mail or e-mail it to the provided address.	Subtotal	\$ 218,750.00
	Discount	
	Sales Tax Rate	% 10.00
	Sales Tax	
	<b>Total inc GST</b>	<b>\$ 240,625.00</b>

Above information is not an invoice and only an estimate of services/goods described above.  
Payment will be collected in prior to provision of services/goods described in this quote.

Please confirm your acceptance of this quote by signing this document

Signature \_\_\_\_\_

Print Name \_\_\_\_\_

Date \_\_\_\_\_

**Thank you for your business!**

Should you have any enquiries concerning this quote, please contact Barry Haden on [REDACTED] 7 738

■ Donaldson St, ■  
 Tel: ■ 7 738 Fax: E-mail: info@ ■  
 BSB: 112879 Account Number : ■ 6 088



Nuix-defined  
Metadata

File Size 141312  
 File Type application/vnd.ms-excel  
 GUID 4806b4bb-5fb0-4bf5-8b36-16b3bf9ee09a  
 Item Date 2018-02-28T16:02:54.000+11:00  
 MD5 Digest 203833a5e60362f6d2ad914b1be6fdef  
 Path Name /E18-0736-AS-7-1-PR-0072/E18-0736-AS-7-1-PR-0072.E01/[Unnamed Disk Image]/Lexar/[File System Root]/blue  
 usb/new Quotes  
 Shannon Entropy 6.534615812908199

User-defined  
Evidence Metadata

Property Source E18-0736-AS-7-1-PR-0072  
 Properties  
 Application Version 983040  
 AppName Microsoft Macintosh Excel  
 Author Euro Maintenance and Civil  
 CLSID {00020820-0000-0000-C000-000000000046}  
 Company Euro Maintenance and Civil  
 Contains false  
 Comments  
 Copyright © 2013 Spreadsheet123 LTD  
 Created 2009-07-28T19:11:35.000Z  
 DocSecurity 0  
 Excel Freeze Panes false  
 Excel Hidden Columns true  
 Excel Hidden Rows true  
 Excel Hidden Sheets false  
 Excel Hidden Sheets Count 0  
 Excel Hidden Workbook false  
 Excel Pivot Tables false  
 Excel Print Areas true  
 Excel Protected Sheets false  
 Excel Very Hidden Sheets false

Excel Very Hidden Sheets Count	0
Excel Workbook BIFF Info	VI=0x10 VN=0x506 Build=28109 Year=1996
Excel Workbook BIFF Version	7
Excel Workbook Write Protected	false
FAT Directory Index	11
FAT Short File Name	ECMDAR~1.XLS
File Accessed	2019-11-27T00:00:00.000+11:00
File Created	2018-02-28T22:52:09.530+11:00
File Modified	2018-02-28T16:02:54.000+11:00
File Offset	2178408448
File Start Cluster	66362
File Start Sector	4254704
Hyperlinks Changed	false
Last Author	Microsoft Office User
Last Printed	2017-12-20T05:46:01.901Z
Last Saved	2018-02-28T05:02:54.878Z
Links Dirty	false
MS-DOS Archive	true
MS-DOS Hidden	false
MS-DOS Read-only	false
MS-DOS System	false
Name	ECM Daroobalgie Quote Sth Bound.xls
Physical Start Sector	4263232
Scale Crop	false
Shared Document	false
Title	Price Quote
Version	1.0.1

## Euro Civil &amp; Maintenance Pty Ltd

Quality is Our Goal



Quote

Date	February 28, 2018
PO #	
Quote #	ECMQ00303
Customer ID	RMS

ABN: 26 604 934 698

**Customer:**

Roads and Maritime Services

Attention: Alexandre Dubois

ABN: 76 236 371 088

110 George St, Parramatta NSW 2150

(02) 8849 2633

## Quote/Project Description

The works Quote involved the following : Daroobalgie

- 1- Installation of toilet cubicle/meeting room and civil works
- 2- Installation concrete pads for weighbridge at Daroobalgie Sth

	Line Total
<b>1- Installation of toilet cubicle/meeting room and civil works</b>	
Carry out utility surveys and DBYD	
Hiring of 80 meters of water filled barriers to block entry to site Sth bound	
Hiring of 120 meters of temporary fencing for excavated areas around the toilet / change room and concreting lead up pavement	
Hire truck with Hiab (crane) for transportation of cubicle from Westmead NSW to Daroobalgie HVIS	
Hire 5 tone Excavator with auger and rock breaker	
Auger of piers and trenching of footings for new location of site toilet / change room	
Supply Aggregate concrete for piers and footings	
Supply Galvanized steel chains and install in concreted piers for anchorage of cubicle	
Hiring of crane to install cubicle over new footing and anchored down.	
Supply 1 x 3500L Bio Septic tank	
Supply 1x 1100 L pump station	
Supply pf 10,000L Collection Well	
Excavate 25m trench and hole for installation of septic tank in ground	
Supply 100mm sewerage pipes for installation from cubicle to septic tank & overflow	
Trench and excavate from septic tank 25m for installation of overflow retention pit	
Excavate level & compact blinding pad for solid base of rainwater tank	
Supply 90mm storm water piping and plumb up from cubicle to tank	
Supply and install electric water pump to cubicle	
Excavate 100m trench to depth of 600mm	
Supply 100m of 1 inch copper pipe	
Plumb water pipe from water meter to cubicle	
Supply and install 3.5 kw air-conditioning split system as requested to toilet/meeting room	
Excavate and formwork for footpath	
Supply concrete and finish footpath to enter cubicle	
Supply truck & Dog to remove unwanted materials	
Supply 9 cubic meter skip bin for removal of rubbish	
Travel, labor hire, accommodation, fuel and expenses	
<b>2- Installation concrete pads for weighbridge at Daroobalgie Sth</b>	
Carry out utility surveys and DBYD	
Excavation of 15 meters of flexible pavement to a depth of 350mm at Sth Bound	
Formwork 13m long by 6m wide to Nth & Sth Bound for concrete pads	
Supply re-enforced steel mesh and rio bars times two layers to Sth bound weighbridge sites	
Supply approx 20 cubic meters of aggregate to each Nth& Sth bound concrete pads = total of 40 cubes	
Finish concrete and screed to RMS requirements for weighing	
Engage surveyor to ensure concreting together with weighbridge meet the Cat 1 requirements	
Supply truck & Dog to remove unwanted materials	
Supply sweeper to clean site and prep for line marking	
Line Marking the perimeter of the newly installed concrete to match current weighbridge line marking	
Paint 5x5 meters stop sign at the Sth bound sites prior to weighbridge	
Install 2 x stop signs with post before weighbridge	
Travel, labor hire, accommodation, fuel and expenses	
<b>Special Notes and Instructions</b>	
Once signed, please Fax, mail or e-mail it to the provided address.	
Subtotal	\$ 218,750.00
Discount	
Sales Tax Rate	% 10.00
Sales Tax	
<b>Total inc GST</b>	<b>\$ 240,625.00</b>

Above information is not an invoice and only an estimate of services/goods described above.  
Payment will be collected in prior to provision of services/goods described in this quote.

Please confirm your acceptance of this quote by signing this document

Signature	Print Name	Date
-----------	------------	------

Thank you for your business!

Should you have any enquiries concerning this quote, please contact Barry Haden on 7 738

Donaldson St. [REDACTED]  
Tel: [REDACTED] 7 738 Fax: E-mail: info@[REDACTED]  
BSB: 112879 Account Number : [REDACTED] 5 088

Nunix-defined	
Metadata	
File Size	37271
File Type	application/pdf
GUID	f52ab3f6-825b-4232-8432-1157849bc5bd
Item Date	2018-03-01T09:40:00.000+11:00
MD5 Digest	c5a98543168078939ccc6687d58e9de1
Path Name	/E18-0736-AS-7-9-PR-0022/E18-0736-AS-7-9-PR-0022.E01/[Unnamed Disk Image]/[Unnamed Partition]/[File System Root]
Shannon Entropy	7.876113750069638
User-defined	
Evidence Metadata	
Property Source	E18-0736-AS-7-9-PR-0022
Properties	
Application Created	2018-02-28T22:40:01.000Z
Application Modified	2018-02-28T22:40:01.000Z
FAT Directory Index	91
FAT Short File Name	ECMDAR~1.PDF
File Accessed	2019-11-27T00:00:00.000+11:00
File Created	2018-03-01T09:40:01.090+11:00
File Modified	2018-03-01T09:40:00.000+11:00
File Offset	21102592
File Start Cluster	823
File Start Sector	41216
MS-DOS Archive	true
MS-DOS Hidden	false
MS-DOS Read-only	false
MS-DOS System	false
Name	ECM Daroobalgie Quote Sth Bound.pdf
Page Count	1
PDF AAPL:Keywords	[]
PDF Certification Level	Not Certified
PDF Contains Annotations	false
PDF Contains Comments	false
PDF Creator	Excel
PDF Encryption Level	None
PDF Images JPEG	1

PDF Javascript Present	false
PDF Metadata Encrypted	false
PDF Portfolio	false
PDF Producer	Mac OS X 10.12.6 Quartz PDFContext
PDF Version	3
Physical Start Sector	41248
Title	ECM Daroobalgie Quote Sth Bound

## ECM Quote Daroobalgie Sth bound

---

**From:** info@[REDACTED]  
**To:** DUBOIS Alexandre <alex.p.dubois@rms.nsw.gov.au>  
**Date:** Thu, 01 Mar 2018 09:43:00 +1100  
**Attachments:** ECM Daroobalgie Quote Sth Bound.pdf (37.27 kB)

---

Hi Alexandre

Please find attached quote for daroobalgie HVIS sth bound Quote

Kind Regards,

Barry Haden  
Director

[REDACTED] Donaldson St [REDACTED]  
[REDACTED]  
[REDACTED]

E: [info@\[REDACTED\]](mailto:info@[REDACTED])  
M: +61 [REDACTED] 7 738

This email is confidential and intended solely for the use of the individual to whom it is addressed. Any views or opinions presented are solely those of the author and do not necessarily represent those of ECM. If you are not the intended recipient, please be advised that forwarding, printing or copying of this email is strictly prohibited. If you have received this email in error please notify our admin on +61 [REDACTED] 7 738

## Euro Civil &amp; Maintenance Pty Ltd

Quality is Our Goal



Quote

Date	February 28, 2018
PO #	
Quote #	ECMQ00303
Customer ID	RMS

ABN: 26 604 934 698

## Customer:

Roads and Maritime Services

Attention: Alexandre Dubois

ABN: 76 236 371 088

110 George St, Parramatta NSW 2150

(02) 8849 2633

## Quote/Project Description

The works Quote involved the following : Daroobalgie

1- Installation of toilet cubicle/meeting room and civil works

2- Installation concrete pads for weighbridge at Daroobalgie Sth

	Line Total
<b>1- Installation of toilet cubicle/meeting room and civil works</b>	
Carry out utility surveys and DBYD	
Hiring of 80 meters of water filled barriers to block entry to site Sth bound	
Hiring of 120 meters of temporary fencing for excavated areas around the toilet / change room and concreting lead up pavement	
Hire truck with Hiab (crane) for transportation of cubicle from Westmead NSW to Daroobalgie HVIS	
Hire 5 tone Excavator with auger and rock breaker	
Auger of piers and trenching of footings for new location of site toilet / change room	
Supply Aggregate concrete for piers and footings	
Supply Galvanized steel chains and install in concreted piers for anchorage of cubicle	
Hiring of crane to install cubicle over new footing and anchored down.	
Supply 1 x 3500L Bio Septic tank	
Supply 1x 1100 L pump station	
Supply pf 10,000L Collection Well	
Excavate 25m trench and hole for installation of septic tank in ground	
Supply 100mm sewerage pipes for installation from cubicle to septic tank & overflow	
Trench and excavate from septic tank 25m for installation of overflow retention pit	
Excavate level & compact blinding pad for solid base of rainwater tank	
Supply 90mm storm water piping and plumb up from cubicle to tank	
Supply and install electric water pump to cubicle	
Excavate 100m trench to depth of 600mm	
Supply 100m of 1 inch copper pipe	
Plumb water pipe from water meter to cubicle	
Supply and install 3.5 kw air-conditioning split system as requested to toilet/meeting room	
Excavate and formwork for footpath	
Supply concrete and finish footpath to enter cubicle	
Supply truck & Dog to remove unwanted materials	
Supply 9 cubic meter skip bin for removal of rubbish	
Travel, labor hire, accommodation, fuel and expenses	
<b>2- Installation concrete pads for weighbridge at Daroobalgie Sth</b>	
Carry out utility surveys and DBYD	
Excavation of 15 meters of flexible pavement to a depth of 350mm at Sth Bound	
Formwork 13m long by 6m wide to Nth & Sth Bound for concrete pads	
Supply re-enforced steel mesh and rio bars times two layers to Sth bound weighbridge sites	
Supply approx 20 cubic meters of aggregate to each Nth& Sth bound concrete pads = total of 40 cubes	
Finish concrete and screed to RMS requirements for weighing	
Engage surveyor to ensure concreting together with weighbridge meet the Cat 1 requirements	
Supply truck & Dog to remove unwanted materials	
Supply sweeper to clean site and prep for line marking	
Line Marking the perimeter of the newly installed concrete to match current weighbridge line marking	
Paint 5x5 meters stop sign at the Sth bound sites prior to weighbridge	
Install 2 x stop signs with post before weighbridge	
Travel, labor hire, accommodation, fuel and expenses	
<b>Special Notes and Instructions</b>	
Once signed, please Fax, mail or e-mail it to the provided address.	
Subtotal	\$ 218,750.00
Discount	
Sales Tax Rate	% 10.00
Sales Tax	
<b>Total inc GST</b>	<b>\$ 240,625.00</b>

Above information is not an invoice and only an estimate of services/goods described above.  
Payment will be collected in prior to provision of services/goods described in this quote.

Please confirm your acceptance of this quote by signing this document

Signature	Print Name	Date
-----------	------------	------

Thank you for your business!

Should you have any enquiries concerning this quote, please contact Barry Haden on 7 738

Donaldson St.  
Tel: 7 738 Fax: E-mail: info@

BSB: 112879 Account Number : 5 088

OZCORP CIVIL

## Quote

Luxford Road

**DATE** March 1, 2018  
**Quote #** 173

ABN: 37 607 800 895 Phone: 2 468

**Bill To:**

Att: Alex Dubois  
 Roads and Maritime Services  
 110 George Street  
 Parramatta NSW 2150  
 02 8837 0636

**Comments or special instructions:** Daroobalgie South Bound HVIS

Description	AMOUNT
<p>This Quote is for Daroobalgie Heavy Vehicle Inspection Bay</p> <p>Scope of works as per RFQ sent on 26/2/2018</p> <ul style="list-style-type: none"> <li>- Transportation of Amenities to site</li> <li>- Provision of utility surveys</li> <li>- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.</li> <li>- Installation of Septic pump tanks as per attached designs and specifications at Daroobalgie Nth bound site.</li> <li>- Installation of amenities block, exact location to be finalised on site by RMS, indicative location of tanks and block shown on attached design.</li> <li>- Excavation for council water supply</li> <li>- Dumping of unwanted materials</li> <li>- Connection of water supply by a licenced plumber.</li> <li>- Excavation and dumping of 15 meters of flexible pavement to a depth of 350mm and allowance for dumping costs at both Daroobalgie Nth and Sth.</li> <li>- Formwork, provision of steel and concreting 13m long by 6 m wide to a depth of 250mm, cross section drawing to be provided at both Daroobalgie Nth and Sth.</li> <li>- Line marking of areas around the newly installed concrete pad in addition to the installation a 5mx5m stop sign at both Nth and Sth bound sites prior to the weighbridge. ( Current stop marker is faded)</li> <li>- Installation of two stop signs with posts</li> <li>- Cleaning of the area and make good.</li> </ul> <p>Travel Allowances + incidentals</p> <p>Accomodation</p>	
<b>TOTAL Ex GST</b>	\$ 227,550.00
<b>TOTAL Inc. GST</b>	\$ 250,305.00

If you have any questions concerning this quotation, KrisTui, 2 468, E-mail: admin

**THANK YOU FOR YOUR BUSINESS!**



## NuiX-defined

## Metadata

File Size	344576
File Type	application/vnd.ms-excel
GUID	5c9a8bfd-9992-4f3e-82f1-554e218e93cd
Item Date	2018-02-28T13:53:36.000+11:00
MD5 Digest	c2053f9bbba7cd2c1576670c91b00f63
Path Name	/E18-0736-AS-7-9-PR-0021/E18-0736-AS-7-9-PR-0021.E01/[Unnamed Disk Image]/STORE N GO/[File System Root]/.Trashes/501/ozcorp items(
Shannon Entropy	7.882230462170328

User-defined  
Evidence Metadata

Property Source	E18-0736-AS-7-9-PR-0021
-----------------	-------------------------

Properties

APAuthor	191
APEditor	92
Application Version	983040
Applications	79;#Template 12;#184;#Office 2000;#182;#Office XP;#23;#Microsoft Office Excel 2007;#22;#Excel 2003
AppName	Microsoft Macintosh Excel
AppVer	
APTrustLevel	1.0000000000000000
AssetId	TS006207086
AssetType	TP
Author	Microsoft Corporation
AuthoringAssetId	TP006207086
BugNumber	GTM: 2/13. GTM Batch 1. 498563
CLSID	{00020820-0000-0000-C000-000000000046}
Company	Microsoft Corporation
Contains	false
Comments	
Content Type	OoFile
ContentTypeId	0x0101006025706CF4CD034688BEBAE97A2E701D020200C3831ACA17D8814887A164412888521E
Created	2000-07-27T22:24:14.000Z
display_urn:schem	
as-microsoft-	
com:office:office#	REDMOND\cynvey
APAuthor	
display_urn:schem	
as-microsoft-	REDMOND\v-luannv

com:office:office#  
 APEditor  
 DocSecurity 0  
 Excel Freeze Panes false  
 Excel Hidden Columns false  
 Excel Hidden Rows false  
 Excel Hidden Sheets false  
 Excel Hidden Sheets Count 0  
 Excel Hidden Workbook false  
 Excel Pivot Tables false  
 Excel Print Areas false  
 Excel Protected Sheets false  
 Excel Very Hidden Sheets false  
 Excel Very Hidden Sheets Count 0  
 Excel Workbook BIFF Info VI=0x10 VN=0x506 Build=28109 Year=1996  
 Excel Workbook BIFF Version 7  
 Excel Workbook Write Protected false  
 FAT Directory Index 277  
 FAT Short File Name ?ZCO~280.XLS  
 File Accessed 2019-01-14T00:00:00.000+11:00  
 File Created 2018-02-28T13:53:37.310+11:00  
 File Modified 2018-02-28T13:53:36.000+11:00  
 File Offset 36110336  
 File Start Cluster 1691  
 File Start Sector 70528  
 Hyperlinks Changed false  
 IsDeleted 0  
 IsSearchable 0  
 Last Author Microsoft Office User  
 Last Printed 2017-12-20T05:47:48.558Z

Last Saved	2018-02-28T02:53:36.585Z
Links Dirty	false
Markets	en-us
Milestone	Continuous
MS-DOS Archive	true
MS-DOS Hidden	false
MS-DOS Read-only	false
MS-DOS System	false
Name	Ozcorp Daroobalgie South bound HVIS.xls
NumericAssetId	
NumericId	-1.0000000000000000
OpenTemplate	1
Physical Start Sector	78592
PrimaryImageGen	1
Provider	EY006220130
PublishStatusLook up	253516
PublishTargets	OfficeOnline
Scale Crop	false
Shared Document	false
ShowIn	Show everywhere
SourceTitle	Price quotation without tax
TemplateStatus	Complete
Title	Price quotation without tax
TPApplication	Excel
TPAppVersion	11
TPClientViewer	Microsoft Office Excel
TPCommandLine	{XL} /t {FilePath}
TPComponent	EXCELFiles
TPFriendlyName	Price quotation without tax
TPInstallLocation	{My Templates}
TPLaunchHelpLink	
TPLaunchHelpLinkType	Template
TPNamespace	EXCEL
TrustLevel	Microsoft Managed Content
UALocRecommendation	Localize
UANotes	389015P. LEGACY FROM TOW; June 2003 retrofit. 447517P



OZCORP CIVIL

## Quote

Luxford Road

**DATE** March 1, 2018  
**Quote #** 173

ABN: 37 607 800 895 Phone: 2 468

**Bill To:**

Att: Alex Dubois  
 Roads and Maritime Services  
 110 George Street  
 Parramatta NSW 2150  
 02 8837 0636

**Comments or special instructions:** Daroobalgie South Bound HVIS

Description	AMOUNT
<p>This Quote is for Daroobalgie Heavy Vehicle Inspection Bay</p> <p>Scope of works as per RFQ sent on 26/2/2018</p> <ul style="list-style-type: none"> <li>- Transportation of Amenities to site</li> <li>- Provision of utility surveys</li> <li>- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.</li> <li>- Installation of Septic pump tanks as per attached designs and specifications at Daroobalgie Nth bound site.</li> <li>- Installation of amenities block, exact location to be finalised on site by RMS, indicative location of tanks and block shown on attached design.</li> <li>- Excavation for council water supply</li> <li>- Dumping of unwanted materials</li> <li>- Connection of water supply by a licenced plumber.</li> <li>- Excavation and dumping of 15 meters of flexible pavement to a depth of 350mm and allowance for dumping costs at both Daroobalgie Nth and Sth.</li> <li>- Formwork, provision of steel and concreting 13m long by 6 m wide to a depth of 250mm, cross section drawing to be provided at both Daroobalgie Nth and Sth.</li> <li>- Line marking of areas around the newly installed concrete pad in addition to the installation a 5mx5m stop sign at both Nth and Sth bound sites prior to the weighbridge. ( Current stop marker is faded)</li> <li>- Installation of two stop signs with posts</li> <li>- Cleaning of the area and make good.</li> </ul> <p>Travel Allowances + incidentals</p> <p>Accomodation</p>	
<b>TOTAL Ex GST</b>	\$ 227,550.00
<b>TOTAL Inc. GST</b>	\$ 250,305.00

If you have any questions concerning this quotation, KrisTui, 2 468, E-mail: admin@

**THANK YOU FOR YOUR BUSINESS!**

## Nuix-defined

## Metadata

File Size 344576  
 File Type application/vnd.ms-excel  
 GUID ff3bc1bb-4992-4b49-a25e-22cfc9efc0ee  
 Item Date 2018-02-28T14:04:38.000+11:00  
 MD5 Digest 511ec65a09287c6953375b037cc8a3ab  
 Path Name /E18-0736-AS-7-1-PR-0072/E18-0736-AS-7-1-PR-0072.E01/[Unnamed Disk Image]/Lexar/[File System Root]/blueusb/new Quotes  
 Shannon Entropy 7.882187833191645

## User-defined

## Evidence Metadata

Property Source E18-0736-AS-7-1-PR-0072  
 Properties  
 APAuthor 191  
 APEditor 92  
 Application Version 983040  
 Applications 79;#Template 12;#184;#Office 2000;#182;#Office XP;#23;#Microsoft Office Excel 2007;#22;#Excel 2003  
 AppName Microsoft Macintosh Excel  
 AppVer  
 APTrustLevel 1.0000000000000000  
 AssetId TS006207086  
 AssetType TP  
 Author Microsoft Corporation  
 AuthoringAssetId TP006207086  
 BugNumber GTM: 2/13. GTM Batch 1. 498563  
 CLSID {00020820-0000-0000-C000-000000000046}  
 Company Microsoft Corporation  
 Contains false  
 Comments  
 Content Type OOFile  
 ContentTypeId 0x0101006025706CF4CD034688BEBAE97A2E701D020200C3831ACA17D8814887A164412888521E  
 Created 2000-07-27T22:24:14.000Z  
 display\_urn:schem  
 as-microsoft-  
 com:office:office# REDMOND\cynvey  
 APAuthor  
 display\_urn:schem  
 as-microsoft- REDMOND\v-luannv

com:office:office#  
 APEditor  
 DocSecurity 0  
 Excel Freeze Panes false  
 Excel Hidden Columns false  
 Excel Hidden Rows false  
 Excel Hidden Sheets false  
 Excel Hidden Sheets Count 0  
 Excel Hidden Workbook false  
 Excel Pivot Tables false  
 Excel Print Areas false  
 Excel Protected Sheets false  
 Excel Very Hidden Sheets false  
 Excel Very Hidden Sheets Count 0  
 Excel Workbook BIFF Info VI=0x10 VN=0x506 Build=28109 Year=1996  
 Excel Workbook BIFF Version 7  
 Excel Workbook Write Protected false  
 FAT Directory Index 27  
 FAT Short File Name OZCORP~3.XLS  
 File Accessed 2019-11-27T00:00:00.000+11:00  
 File Created 2018-02-28T22:52:09.690+11:00  
 File Modified 2018-02-28T14:04:38.000+11:00  
 File Offset 2178867200  
 File Start Cluster 66376  
 File Start Sector 4255600  
 Hyperlinks Changed false  
 IsDeleted 0  
 IsSearchable 0  
 Last Author Microsoft Office User  
 Last Printed 2017-12-20T05:47:48.558Z

Last Saved	2018-02-28T03:04:39.165Z
Links Dirty	false
Markets	en-us
Milestone	Continuous
MS-DOS Archive	true
MS-DOS Hidden	false
MS-DOS Read-only	false
MS-DOS System	false
Name	Ozcorp Daroobalgie South bound HVIS.xls
NumericAssetId	
NumericId	-1.0000000000000000
OpenTemplate	1
Physical Start Sector	4264128
PrimaryImageGen	1
Provider	EY006220130
PublishStatusLook up	253516
PublishTargets	OfficeOnline
Scale Crop	false
Shared Document	false
ShowIn	Show everywhere
SourceTitle	Price quotation without tax
TemplateStatus	Complete
Title	Price quotation without tax
TPApplication	Excel
TPAppVersion	11
TPClientViewer	Microsoft Office Excel
TPCommandLine	{XL} /t {FilePath}
TPComponent	EXCELFiles
TPFriendlyName	Price quotation without tax
TPInstallLocation	{My Templates}
TPLaunchHelpLink	
TPLaunchHelpLinkType	Template
TPNamespace	EXCEL
TrustLevel	Microsoft Managed Content
UALocRecommendation	Localize
UANotes	389015P. LEGACY FROM TOW; June 2003 retrofit. 447517P





Luxford Road

**DATE** March 1, 2018  
**Quote #** 174

ABN: 37 607 800 895 Phone: 2 468

**Bill To:**

Att: Alex Dubois  
 Roads and Maritime Services  
 110 George Street  
 Parramatta NSW 2150  
 02 8837 0636

**Comments or special instructions:** Daroobalgie South Bound HVIS

Description	AMOUNT
<p>This Quote is for Daroobalgie Heavy Vehicle Inspection Bay</p> <p>Scope of works as per RFQ sent on 26/2/2018</p> <ul style="list-style-type: none"> <li>- Site establishment</li> <li>- Provision of barricading site with temporary fencing and warning signage</li> <li>- Transportation of Amenities to site</li> <li>- Provision of utility surveys</li> <li>- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.</li> </ul> <p>Installation of septic pump tanks as per attached designs and specification at Daroobalgie Sth bound site</p> <ul style="list-style-type: none"> <li>- Installation of amenities block, exact location to be finalized on site by RMS, Indicative location of tanks and blocks shown on attached design</li> <li>- Excavation for council water supply</li> <li>- Connection of water supply by licensed plumber</li> <li>- Excavation and dumping of 30 tonnes of flexible pavement to a depth of 350mm Daroobalgie Sth bound screening lane</li> <li>- Dumping of unwanted materials</li> <li>- Formwork, provisions of steel and concreting 13m long by 6m wide to a depth of 250mm</li> <li>- Line marking of areas around newly installed concrete pad in addition to installation a 5mx5m thermal plastic stop sign on ground prior to weighbridge</li> </ul> <p>Cleaning of site and make good</p> <p>Travel Allowances + incidentals</p> <p>Accommodation</p>	
<b>TOTAL Ex GST</b>	\$ 225,000.00
<b>TOTAL Inc. GST</b>	\$ 247,500.00

If you have any questions concerning this quotation, KrisTui, 2 468, E-mail: admin@

**THANK YOU FOR YOUR BUSINESS!**

Nunix-defined	
Metadata	
File Size	25024
File Type	application/pdf
GUID	2d5fe812-2318-441a-b6de-c975ebdcc86b
Item Date	2018-03-01T12:07:44.000+11:00
MD5 Digest	a8a718f742bf9457600f5389c9ff59b9
Path Name	/E18-0736-AS-7-9-PR-0022/E18-0736-AS-7-9-PR-0022.E01/[Unnamed Disk Image]/[Unnamed Partition]/[File System Root]/?RASHE~1.J2Z/?01
Shannon Entropy	7.745450740318571
User-defined	
Evidence Metadata	
Property Source	E18-0736-AS-7-9-PR-0022
Properties	
Application Created	2018-03-01T01:07:45.000Z
Application Modified	2018-03-01T01:07:45.000Z
FAT Directory Index	209
FAT Short File Name	?ZCO~212.PDF
File Accessed	2019-01-09T00:00:00.000+11:00
File Created	2018-03-01T12:07:45.710+11:00
File Modified	2018-03-01T12:07:44.000+11:00
File Offset	26771456
File Start Cluster	1169
File Start Sector	52288
MS-DOS Archive	true
MS-DOS Hidden	false
MS-DOS Read-only	false
MS-DOS System	false
Name	Ozcorp Daroobalgie South bound HVIS.pdf
Page Count	1
PDF	
AAPL:Keywords	[]
PDF Certification Level	Not Certified
PDF Contains Annotations	false
PDF Contains Comments	false
PDF Creator	Excel
PDF Encryption Level	None

PDF Javascript Present	false
PDF Metadata Encrypted	false
PDF Portfolio	false
PDF Producer	Mac OS X 10.11.6 Quartz PDFContext
PDF Version	3
Physical Start Sector	52320
Title	Ozcorp Darroobalgie South bound HVIS

## Ozcorp Civil Daroobalgie Sth Bound Quote

---

**From:** oz corp civil <admin@[REDACTED]>  
**To:** DUBOIS Alexandre <alex.p.dubois@rms.nsw.gov.au>  
**Date:** Thu, 01 Mar 2018 12:13:17 +1100  
**Attachments:** Ozcorp Daroobalgie South bound HVIS.pdf (25.02 kB)

---

Hi Alexandre

Please find ozcorp civil Quote for Daroobalgie Sth Bound HVIB

Regards,

Kris Tui  
Director  
MOB: [REDACTED] 5 965  
EMAIL: Admin@[REDACTED]

IMPORTANT: The contents of this email and any attachments are confidential. They are intended for the named recipient(s) only. If you have received this email by mistake, please notify the sender immediately and do not the contents to anyone or make copies thereof.

Luxford Road

**DATE** March 1, 2018  
**Quote #** 174

ABN: 37 607 800 895 Phone: 2 468

**Bill To:**

Att: Alex Dubois  
 Roads and Maritime Services  
 110 George Street  
 Parramatta NSW 2150  
 02 8837 0636

**Comments or special instructions:** Daroobalgie South Bound HVIS

Description	AMOUNT
<p>This Quote is for Daroobalgie Heavy Vehicle Inspection Bay</p> <p>Scope of works as per RFQ sent on 26/2/2018</p> <ul style="list-style-type: none"> <li>- Site establishment</li> <li>- Provision of barricading site with temporary fencing and warning signage</li> <li>- Transportation of Amenities to site</li> <li>- Provision of utility surveys</li> <li>- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.</li> </ul> <p>Installation of septic pump tanks as per attached designs and specification at Daroobalgie Sth bound site</p> <ul style="list-style-type: none"> <li>- Installation of amenities block, exact location to be finalized on site by RMS, Indicative location of tanks and blocks shown on attached design</li> <li>- Excavation for council water supply</li> <li>- Connection of water supply by licensed plumber</li> <li>- Excavation and dumping of 30 tonnes of flexible pavement to a depth of 350mm Daroobalgie Sth bound screening lane</li> <li>- Dumping of unwanted materials</li> <li>- Formwork, provisions of steel and concreting 13m long by 6m wide to a depth of 250mm</li> <li>- Line marking of areas around newly installed concrete pad in addition to installation a 5mx5m thermal plastic stop sign on ground prior to weighbridge</li> </ul> <p>Cleaning of site and make good</p> <p>Travel Allowances + incidentals</p> <p>Accommodation</p>	
<b>TOTAL Ex GST</b>	\$ 225,000.00
<b>TOTAL Inc. GST</b>	\$ 247,500.00

If you have any questions concerning this quotation, KrisTui, 2 468, E-mail: admin@

**THANK YOU FOR YOUR BUSINESS!**

## CBF PROJECTS PTY LTD

## Quote

Elouera Crescent [REDACTED]  
 Telephone: (02) [REDACTED] 8462  
 Mobile: [REDACTED] 4 333  
 ABN: 78 159 482 210

Date: March 2, 2018  
 Quote #: Q305

To: Road and Maritime Services

99 Phillip St  
 Parramatta NSW 2150

Mob: [REDACTED] 6 298 Ph: 8837 0636

Fax : 8849 2522

Project manager: A. Dubois

Email: Alex.p.Dubois@rms.nsw.gov.au

ABN 76 236 371 088

## Salesperson

## Job

## Payment Terms

Chahid Chahine	Daroobalgie Inspection station Sth bound	
----------------	--	--

Qty	Unit	Description	Unit Price	Line Total
		<b>Daroobalgie</b>		
	EA	Establishment		
		<b>Amenities Installation</b>		
		<b>Plant Equipment</b>		
		Hiring of Crane for the delivery of Septic tank within the excavated area		
		Truck and Dog for the removal of unwanted materials		
		Hiring of Bobcat with sweeper to clean site once septic and collection well have been installed		
		<b>Concrete</b>		
		Supply and lay concrete for base of septic tank		
		Supply approx 80 cubes of concrete for the weighbridge pads		
		<b>Materials</b>		
		Procure and install steel re-enforced bars to concrete pads		
		Supply Formwork for concrete weighbridge pad and concrete footpath to amenities building		
		Temporary fence all excavated areas - allowance has been made for approx 150m		
		Supply water filled barriers to ensure Nth and Sth bound sites are closed off for the entire work period, approx 14 days has been provisioned		
		supply thermal plastic paint and install 5 x 5 meter stop signs at both Nth and Sth bound sites prior to weighbridge		
		Supply 2 x stop signs with post and install		

[illegible]



## Nuix-defined Metadata

File Size	35328
File Type	application/vnd.ms-excel
GUID	07677973-04dc-4078-a104-21367703067c
Item Date	2018-02-28T11:25:40.000+11:00
MD5 Digest	b6dde52553993d0fb963598fb364d1e0
Path Name	/E18-0736-AS-7-9-PR-0024/E18-0736-AS-7-9-PR-0024.E01/[Unnamed Disk Image]/[Unnamed Partition]/[File System Root]
Shannon Entropy	5.060899707274054
User-defined Evidence Metadata	
Property Source	E18-0736-AS-7-9-PR-0024
Properties	
_AdHocReviewCycleID	-2109409232
_AuthorEmail	Alexandre_DUBOIS@rta.nsw.gov.au
_AuthorEmailDisplayName	DUBOIS Alexandre
_EmailSubject	Armco
_NewReviewCycle	
_ReviewingToolsShownOnce	
_TemplateID	TC101514371033
Application Version	983040
AppName	Microsoft Macintosh Excel
Author	
CLSID	{00020820-0000-0000-C000-000000000046}
Comments	
Company	Microsoft Corporation
Contains Comments	false
Created	2006-01-23T19:37:33.000Z
DocSecurity	0
Excel Freeze Panes	false
Excel Hidden Columns	false
Excel Hidden Rows	false
Excel Hidden Sheets	false
Excel Hidden Sheets Count	0
Excel Hidden Workbook	false
Excel Pivot Tables	false
Excel Print Areas	true
Excel Protected Sheets	false
Excel Very Hidden Sheets	false
Excel Very Hidden Sheets Count	0

Excel Workbook BIFF Info	VI=0x10 VN=0x506 Build=28109 Year=1996
Excel Workbook BIFF Version	7
Excel Workbook Write Protected	false
FAT Directory Index	187
File Accessed	2018-02-28T00:00:00.000+11:00
File Created	2018-02-18T13:07:10.220+11:00
File Modified	2018-02-28T11:25:40.000+11:00
File Offset	24379392
File Start Cluster	1023
File Start Sector	47616
Hyperlinks Changed	false
Keywords	
Last Author	Microsoft Office User
Last Printed	2017-12-20T05:39:28.653Z
Last Saved	2018-02-28T03:03:57.949Z
Links Dirty	false
Manager	
MS-DOS Archive	true
MS-DOS Hidden	false
MS-DOS Read-only	false
MS-DOS System	false
Name	?CFD3A00
Physical Start Sector	47648
Scale Crop	false
Shared Document	false
Subject	
Title	

## CBF PROJECTS PTY LTD

## Quote

Elouera Crescent [REDACTED]  
 Telephone: [REDACTED] 8462  
 Mobile: [REDACTED] 4 333  
 ABN: 78 159 482 210

Date: March 2, 2018  
 Quote #: Q305

To: Road and Maritime Services

99 Phillip St  
 Parramatta NSW 2150

Mob: [REDACTED] 6 298 Ph: 8837 0636

Fax : 8849 2522

Email: Alex.p.Dubois@rms.nsw.gov.au

ABN 76 236 371 088

Project manager: A. Dubois

## Salesperson

## Job

## Payment Terms

Chahid Chahine	Daroobalgie Inspection station Sth bound	
----------------	--	--

Qty	Unit	Description	Unit Price	Line Total
		<b>Daroobalgie</b>		
	EA	Establishment		
		<b>Amenities Installation</b>		
		<b>Plant Equipment</b>		
		Hiring of Crane for the delivery of Septic tank within the excavated area		
		Truck and Dog for the removal of unwanted materials		
		Hiring of Bobcat with sweeper to clean site once septic and collection well have been installed		
		<b>Concrete</b>		
		Supply and lay concrete for base of septic tank		
		Supply approx 80 cubes of concrete for the weighbridge pads		
		<b>Materials</b>		
		Procure and install steel re-enforced bars to concrete pads		
		Supply Formwork for concrete weighbridge pad and concrete footpath to amenities building		
		Temporary fence all excavated areas - allowance has been made for approx 150m		
		Supply water filled barriers to ensure Nth and Sth bound sites are closed off for the entire work period, approx 14 days has been provisioned		
		supply thermal plastic paint and install 5 x 5 meter stop signs at both Nth and Sth bound sites prior to weighbridge		
		Supply 2 x stop signs with post and install		

[illegible]

## Nuix-defined Metadata

File Size	33792
File Type	application/vnd.ms-excel
GUID	17348176-ad90-4658-8dc2-8c501c8c810c
Item Date	2018-02-28T13:56:18.000+11:00
MD5 Digest	a21a3da07bece8ce53d6a14e98f727d7
Path Name	/E18-0736-AS-7-9-PR-0032-UsersFolder/E18-0736-AS-7-9-PR-0032-UsersFolder.Lx01/cbfprojectsptyltd/Documents
Shannon Entropy	4.9427967950761165

User-defined Evidence Metadata

Property Source	E18-0736-AS-7-9-PR-0032
-----------------	-------------------------

Properties

_AdHocReviewCycleID	-2109409232
_AuthorEmail	Alexandre_DUBOIS@rta.nsw.gov.au
_AuthorEmailDisplayName	DUBOIS Alexandre
_EmailSubject	Armco
_NewReviewCycle	
_ReviewingToolsShownOnce	
_TemplateID	TC101514371033
Application Version	983040
AppName	Microsoft Macintosh Excel
Author	
CLSID	{00020820-0000-0000-C000-00000000000046}
Comments	
Company	Microsoft Corporation
Contains Comments	false
Created	2006-01-23T19:37:33.000Z
DocSecurity	0
Excel Freeze Panes	false
Excel Hidden Columns	false
Excel Hidden Rows	false
Excel Hidden Sheets	false
Excel Hidden Sheets Count	0
Excel Hidden Workbook	false
Excel Pivot Tables	false
Excel Print Areas	true
Excel Protected Sheets	false
Excel Very Hidden Sheets	false
Excel Very Hidden Sheets Count	0
Excel Workbook BIFF Info	VI=0x10 VN=0x506 Build=28109 Year=1996

Excel Workbook BIFF Version	7
Excel Workbook Write Protected	false
File Accessed	2018-10-25T22:38:04.000Z
File Changed	2018-02-28T02:56:18.000Z
File Created	2018-02-28T02:56:18.000Z
File Modified	2018-02-28T02:56:18.000Z
Hyperlinks Changed	false
Keywords	
Last Author	Microsoft Office User
Last Printed	2017-12-20T05:39:28.653Z
Last Saved	2018-02-28T02:56:18.720Z
Links Dirty	false
Manager	
Name	CBF Daroobalgie Sthbound Quote.xls
Original MD5 Digest	a21a3da07bece8ce53d6a14e98f727d7
Scale Crop	false
Shared Document	false
Subject	
Title	

## CBF PROJECTS PTY LTD

## Quote

Elouera Crescent [REDACTED]  
 Telephone: [REDACTED] 8462  
 Mobile: [REDACTED] 4 333  
 ABN: 78 159 482 210

Date: March 2, 2018  
 Quote #: Q305

To: Road and Maritime Services

99 Phillip St  
 Parramatta NSW 2150

Mob: [REDACTED] 6 298

Ph: 8837 0636

Fax : 8849 2522

Email: Alex.p.Dubois@rms.nsw.gov.au

ABN 76 236 371 088

Project manager: A. Dubois

## Salesperson

## Job

## Payment Terms

Chahid Chahine	Daroobalgie Inspection station Sth bound	
----------------	--	--

Qty	Unit	Description	Unit Price	Line Total
		<b>Daroobalgie</b>		
	EA	Establishment		
		<b>Amenities Installation</b>		
		<b>Plant Equipment</b>		
		Hiring of Crane for the delivery of Septic tank within the excavated area		
		Truck and Dog for the removal of unwanted materials		
		Hiring of Bobcat with sweeper to clean site once septic and collection well have been installed		
		<b>Concrete</b>		
		Supply and lay concrete for base of septic tank		
		Supply approx 80 cubes of concrete for the weighbridge pads		
		<b>Materials</b>		
		Procure and install steel re-enforced bars to concrete pads		
		Supply Formwork for concrete weighbridge pad and concrete footpath to amenities building		
		Temporary fence all excavated areas - allowance has been made for approx 150m		
		Supply water filled barriers to ensure Nth and Sth bound sites are closed off for the entire work period, approx 14 days has been provisioned		
		supply thermal plastic paint and install 5 x 5 meter stop signs at both Nth and Sth bound sites prior to weighbridge		
		Supply 2 x stop signs with post and install		

[illegible]



## NuiX-defined Metadata

File Size	33792
File Type	application/vnd.ms-excel
GUID	d1c31dc9-25b1-4149-a462-b017ca67b4fe
Item Date	2018-02-28T14:03:56.000+11:00
MD5 Digest	c788766aa4e87c7c72c5f956c8ac045b
Path Name	/E18-0736-AS-7-1-PR-0072/E18-0736-AS-7-1-PR-0072.E01/[Unnamed Disk Image]/Lexar/[File System Root]/blue usb/new Quotes
Shannon Entropy	4.945017997859453
User-defined Evidence Metadata	
Property Source	E18-0736-AS-7-1-PR-0072
Properties	
_AdHocReviewCycleID	-2109409232
_AuthorEmail	Alexandre_DUBOIS@rta.nsw.gov.au
_AuthorEmailDisplayName	DUBOIS Alexandre
_EmailSubject	Armco
_NewReviewCycle	
_ReviewingToolsShownOnce	
_TemplateID	TC101514371033
Application Version	983040
AppName	Microsoft Macintosh Excel
Author	
CLSID	{00020820-0000-0000-C000-000000000046}
Comments	
Company	Microsoft Corporation
Contains Comments	false
Created	2006-01-23T19:37:33.000Z
DocSecurity	0
Excel Freeze Panes	false
Excel Hidden Columns	false
Excel Hidden Rows	false
Excel Hidden Sheets	false
Excel Hidden Sheets Count	0
Excel Hidden Workbook	false
Excel Pivot Tables	false
Excel Print Areas	true
Excel Protected Sheets	false
Excel Very Hidden Sheets	false
Excel Very Hidden Sheets Count	0

Excel Workbook BIFF Info	VI=0x10 VN=0x506 Build=28109 Year=1996
Excel Workbook BIFF Version	7
Excel Workbook Write Protected	false
FAT Directory Index	31
FAT Short File Name	CBFDAR~1.XLS
File Accessed	2019-11-27T00:00:00.000+11:00
File Created	2018-02-28T22:52:09.750+11:00
File Modified	2018-02-28T14:03:56.000+11:00
File Offset	2179227648
File Start Cluster	66387
File Start Sector	4256304
Hyperlinks Changed	false
Keywords	
Last Author	Microsoft Office User
Last Printed	2017-12-20T05:39:28.653Z
Last Saved	2018-02-28T03:03:57.949Z
Links Dirty	false
Manager	
MS-DOS Archive	true
MS-DOS Hidden	false
MS-DOS Read-only	false
MS-DOS System	false
Name	CBF Daroobalgie Sth bound Quote.xls
Physical Start Sector	4264832
Scale Crop	false
Shared Document	false
Subject	
Title	



**CBF PROJECTS pty ltd**  
CIVIL BUILDING & FABRICATION

Elouera Crescent [REDACTED]  
Telephone: [REDACTED] 8462  
Mobile: [REDACTED] 4 333  
ABN: 78 159 482 210

# Quote

Date: March 1, 2018  
Quote #: Q305

To: Road and Maritime Services

99 Phillip St  
Parramatta NSW 2150

Mob: [REDACTED] 6 298 Ph: 8837 0636

Fax : 8849 2522

Email: Alex.p.Dubois@rms.nsw.gov.au

ABN 76 236 371 088

Project manager: A. Dubois

**Salesperson**

**Job**

**Payment Terms**

Chahid Chahine	Daroobalgie Inspection station Sth bound	
----------------	--	--

Qty	Unit	Description	Unit Price	Line Total
		<b>Daroobalgie</b>		
	EA	Establishment		
		<b>Amenities Installation</b>		
		<b>Plant Equipment</b>		
		Hiring of Crane for the delivery of Septic tank within the excavated area		
		Truck and Dog for the removal of unwanted materials		
		Hiring of Bobcat with sweeper to clean site once septic and collection well have been installed		
		<b>Concrete</b>		
		Supply and lay concrete for base of septic tank		
		Supply approx 80 cubes of concrete for the weighbridge pads		
		<b>Materials</b>		
		Procure and install steel re-enforced bars to concrete pads		
		Supply Formwork for concrete weighbridge pad and concrete footpath to amenities building		
		Temporary fence all excavated areas - allowance has been made for approx 150m		
		Supply water filled barriers to ensure Nth and Sth bound sites are closed off for the entire work period, approx 14 days has been provisioned		
		supply intermar plastic paint and install 5 x 5 meter stop signs at both Nth and Sth bound sites prior to weighbridge		
		Supply 2 x stop signs with post and install		
		Supply of plumbing materials		
		<b>Installation and civil work</b>		

[illegible]

## Nux-defined Metadata

File Size	62464
File Type	application/vnd.ms-excel
GUID	a7c9b042-a878-48bd-b137-36b1521f111d
Item Date	2018-03-01T10:53:16.000+11:00
MD5 Digest	bde75ab00b56f64b0123499bc358a8ec
Path Name	/E18-0736-AS-7-9-PR-0022/E18-0736-AS-7-9-PR-0022.E01/[Unnamed Disk Image]/[Unnamed Partition]/[File System Root]
Shannon Entropy	6.708477550114876
User-defined Evidence Metadata	
Property Source	E18-0736-AS-7-9-PR-0022
Properties	
_AdHocReviewCycleID	-2109409232
_AuthorEmail	Alexandre_DUBOIS@rta.nsw.gov.au
_AuthorEmailDisplayName	DUBOIS Alexandre
_EmailSubject	Armco
_NewReviewCycle	
_ReviewingToolsShownOnce	
_TemplateID	TC101514371033
Application Version	983040
AppName	Microsoft Macintosh Excel
Author	
CLSID	{00020820-0000-0000-C000-000000000046}
Comments	
Company	Microsoft Corporation
Contains Comments	false
Created	2006-01-23T19:37:33.000Z
DocSecurity	0
Excel Freeze Panes	false
Excel Hidden Columns	false
Excel Hidden Rows	false
Excel Hidden Sheets	false
Excel Hidden Sheets Count	0
Excel Hidden Workbook	false
Excel Pivot Tables	false
Excel Print Areas	true
Excel Protected Sheets	false
Excel Very Hidden Sheets	false
Excel Very Hidden Sheets Count	0

Excel Workbook BIFF Info	VI=0x10 VN=0x506 Build=28109 Year=1996
Excel Workbook BIFF Version	7
Excel Workbook Write Protected	false
FAT Directory Index	26
FAT Short File Name	CBFDAR~1.XLS
File Accessed	2019-11-27T00:00:00.000+11:00
File Created	2018-03-01T10:53:16.140+11:00
File Modified	2018-03-01T10:53:16.000+11:00
File Offset	24477696
File Start Cluster	1029
File Start Sector	47808
Hyperlinks Changed	false
Keywords	
Last Author	Microsoft Office User
Last Printed	2018-02-28T23:51:32.334Z
Last Saved	2018-02-28T23:53:16.268Z
Links Dirty	false
Manager	
MS-DOS Archive	true
MS-DOS Hidden	false
MS-DOS Read-only	false
MS-DOS System	false
Name	CBF Daroobalgie Sth bound Quote.xls
Physical Start Sector	47840
Scale Crop	false
Shared Document	false
Subject	
Title	

## CBF Quote Daroobalgie Sth

---

**From:** cbf projects <info@cbfprojects.com>  
**To:** DUBOIS Alexandre <alex.p.dubois@rms.nsw.gov.au>  
**Date:** Thu, 01 Mar 2018 10:51:51 +1100

---

Hi Alex

Please find quote attached as per RFQ at Daroobalgie sth Newell Hwy

Regards

Director  
chahid chahine  
C B F projects pty ltd

**IMPORTANT NOTICE:** This e-mail and any attachment to it are intended only to be read or used by the named addressee. It is confidential and may contain legally privileged information. No confidentiality or privilege is waived or lost by any mistaken transmission to you. (CBF) is not responsible for any unauthorised alterations to this e-mail or attachment to it. Views expressed in this message are those of the individual sender, and are not necessarily the views of CBF. If you receive this e-mail in error, please immediately delete it from your system and notify the sender. You must not disclose, copy or use any part of this e-mail if you are not the intended recipient.





**CBF PROJECTS pty ltd**  
CIVIL BUILDING & FABRICATION

Elouera Crescent [REDACTED]  
Telephone: (02) 4626 8462  
Mobile: [REDACTED] 4 333

ABN: 78 159 482 210

# Quote

**Date:** March 1, 2018  
**Quote #:** Q305

**To:** Road and Maritime Services

99 Phillip St  
Parramatta NSW 2150

Mob: [REDACTED] 6 298

Ph: 8837 0636

Fax : 8849 2522

Email: Alex.p.Dubois@rms.nsw.gov.au

ABN 76 236 371 088

**Project manager:** A. Dubois

**Salesperson**

**Job**

**Payment Terms**

Chahid Chahine

Daroobalgie Inspection station Sth bound

Qty	Unit	Description	Unit Price	Line Total
		<b>Daroobalgie</b>		
	EA	Establishment		
		<b>Amenities Installation</b>		
		<b>Plant Equipment</b>		
		Hiring of Crane for the delivery of Septic tank within the excavated area		
		Truck and Dog for the removal of unwanted materials		
		Hiring of Bobcat with sweeper to clean site once septic and collection well have been installed		
		<b>Concrete</b>		
		Supply and lay concrete for base of septic tank		
		Supply approx 80 cubes of concrete for the weighbridge pads		
		<b>Materials</b>		
		Procure and install steel re-enforced bars to concrete pads		
		Supply Formwork for concrete weighbridge pad and concrete footpath to amenities building		
		Temporary fence all excavated areas - allowance has been made for approx 150m		
		Supply water filled barriers to ensure Nth and Sth bound sites are closed off for the entire work period, approx 14 days has been provisioned		
		supply thermal plastic paint and install 5 x 5 meter stop signs at both Nth and Sth bound sites prior to weighbridge		
		Supply 2 x stop signs with post and install		
		Supply of plumbing materials		
		<b>Installation and civil work</b>		
		DBYD and utility survey checks to be carried out		
		Install plumbing from main to amenity		
		Install 3550L septic tank as per RFQ		
		Install 1100L Pump station as per RFQ		
		Install 10,000L collection well as per RFQ		



[illegible]



Transport  
for NSW

## Roads and Maritime Services

### Contract Creation & Variation

Is this a CM21 contract? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	Request type: <input checked="" type="checkbox"/> Create new <input type="checkbox"/> Amend existing
--	--

#### Contract variation ONLY details

For contract variation only. Please tick as applicable and fill in details below as required.

<input type="checkbox"/> New value <input type="checkbox"/> New date	Equip purchase order number OR contract number:
--	--

#### Contract details

Supplier: Euro Civil and Maintenance	Supplier No.:
Vendor ABN: 26 604 934 698	
Does the Contract require ERS/RCTI? (PO purposes)	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No
Contract title: (Please include CM21 number on the title of CM21 contracts)	Concrete, Civil works on Newell Highway Sth bound WHS issues
Effective date: 1 Mar 2018	Expiry date: 30 Jun 2018
Contract type:	<input type="checkbox"/> Council <input checked="" type="checkbox"/> CM21 <input type="checkbox"/> Discrete <input type="checkbox"/> Supply Agreement <input checked="" type="checkbox"/> Panel
Payment terms: 30 days from the date of invoice Category:	
<input type="checkbox"/> Payment claim under Security & Payment Act (15 day payment term - SOPA)	

#### Financial details

Awarded amount (ex GST): \$218,750	Initial contract amount:
Contract contingency (if applicable):	Expenditure type: Capex
Total Contract amount (Awarded amount + Contingency): \$218,750	Hierarchical type: Panel
Material Group (UNSPSC product category): 72000000	
Variation amount (excluding approved contract value):	
WBS code: P.0018688.29	Cost centre: 2935
G/L code: 513140	
Agency: <input type="checkbox"/> Cluster wide – 9000 <input type="checkbox"/> TfNSW – 1000 <input checked="" type="checkbox"/> RMS – 3000	
Purchasing group (Region): Sydney	
Notice period (in days) 30 days by default:	
Requesting/Requesting officer name: Alexandre Dubois	

#### Internal stakeholder details

Initiator (Business sponsor):
Contract manager: Alexandre Dubois
Procurement owner: Alexandre Dubois
Contractor stakeholder visibility (Team Tab):

**CLID line item details – Min. requirement of 1 line (\* Mandatory fields)**

<b>Name Line #1</b> (max 40 character limit)* Concrete, Civil works on Newell Highway Sth bound WHS issues			
Description*:			
Unit of measure*:	Each	Target quantity*:	1.0
		Price:	\$218,750
Long text*:			
Supplier part no.*:		Material Group (UNSPSC product category):	

<b>Name Line #2</b> (max 40 character limit)*			
Description*:			
Unit of measure*:		Target quantity*:	
		Price:	
Long text*:			
Supplier part no.*:		Material Group (UNSPSC product category):	

<b>Name Line #3</b> (max 40 character limit)*			
Description*:			
Unit of measure*:		Target quantity*:	
		Price:	
Long text*:			
Supplier part no.*:		Material Group (UNSPSC product category):	

**To be completed only if any other form of approval documentation not attached such as "Letter of Acceptance"**

<b>Requested by :</b> Requester <b>cannot</b> be a Business Partner		<b>Delegated Approval by:</b> Delegation <b>must</b> cover the total value of the PO	
Name: Alexandre Dubois		Name: Craig Steyn	
Staff ID: 00965213		Staff ID: 00961247	Delegation Level: 4
Position: Heavy Vehicle Project & Support Officer		Position: Manager Heavy Vehicle Programs	
Phone No: 02 8837 0636		Phone No: 02 8837 0687	
Signature: 	Date: 1/3/18	Signature*: 	Date: 1.3.2018

**Guidelines**

This form must be used for:

- Creation and variation of all types of contracts in Equip for RMS
- Variation of purchase orders attached to a contract in Equip

All fields are mandatory unless stated "as applicable".  
Documentation to be attached with the contracts are:

- Letter of acceptance
- Tender assessment report
- Pricing schedules

The form along with the documentation should be forwarded to [TSS.RMSContracts@transport.nsw.gov.au](mailto:TSS.RMSContracts@transport.nsw.gov.au)

**For assistance in the completion of these forms please contact [TSS.RMSContracts@transport.nsw.gov.au](mailto:TSS.RMSContracts@transport.nsw.gov.au)**

## Disclosure of Information

Class 1 Contract	
Contract No/ID :	17.0000302935.1100-0034
Equip Contract No :	17.0000302935.1100
Contract Description :	Panel for HVEP- WHS items Newell Hwy Enforcement site
Contract Commencement Date :	01/03/2018
Period of Contract:	20 weeks
Contractor:	EURO CIVIL & MAINTENANCE PTY LTD
Contractor Address:	EURO CIVIL & MAINTENANCE PTY LTD, [REDACTED] Donaldson Street, [REDACTED]
Trading Name:	
Trading Name Address:	
Estimated Payable (\$ Incl GST) :	\$ 240,625.00
Method of Tendering:	Limited (Single Invitation / Selective/WADs)

- Particulars of any related body corporate (within the meaning of the Corporations Act 2001 of the Commonwealth) in respect of the contractor, or any other private sector entity in which the contractor has an interest, that will be involved in carrying out any of the contractor's obligations under the contract or will receive a benefit under the contract

NA

- A description of any provisions under which the amount payable to the contractor may be varied

No provisions under which the amount payable to the contractor may be varied

- A description of any provisions with respect to the renegotiation of the contract

No provisions with respect to the renegotiation of the contract

- In the case of a contract arising from a tendering process, a summary of the criteria against which the various tenders were assessed

Price, experience, panel contractor

- A description of any provisions under which it is agreed that the contractor is to receive payment for providing operational or maintenance services

NA

- **The reason why the contract has provisions which exclude or modify application of Part 4  
Proportionate liability of the Civil**

NA

---

## Work Order 17.0000302935.1100-0015

This document is a Work Order issued under your Work-as-Ordered Contract with RMS dated 31/10/2017 for the Installation of Amenities Block and Civil works at Daroobalgie HVIS.

Under this Work Order, you are requested to carry out the work or services described below ('Contracted Work') on the terms of your Work-as-Ordered Contract and this Work Order.

### **Contracted Work**

Roads and Maritime sought through an RFQ sent on the 26<sup>th</sup> of feb 2018 the submission of a lump sum fee estimate for the installation of Amenities block and the concrete of pavement on the approach to the weighbridge at Daroobalgie HVIS Sth bound on the Newell High way.

The works involve the following:

- Transportation of Amenities to site
- Utility surveys
- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.
- Installation of Septic pump tanks as per attached designs and specifications at Daroobalgie Nth bound site.
- Installation of amenities block, exact location to be finalised on site by RMS, indicative location of tanks and block shown on attached design.
- Excavation for council water supply
- Dumping of unwanted materials
- Connection of water supply by a licenced plumber.
- Excavation and dumping of 15 meters of flexible pavement to a depth of 350mm and allowance for dumping costs at both Daroobalgie Nth and Sth.
- Formwork, provision of steel and concreting 13m long by 6 m wide to a depth of 250mm, cross section drawing to be provided at both Daroobalgie Nth and Sth.
- Line marking of areas around the newly installed concrete pad in addition to the installation a 5mx5m stop sign at both Nth and Sth bound sites prior to the weighbridge.( Current stop marker is faded)
- Installation of two stop signs with posts
- Cleaning of the area and make good.


## Work Order Specific Requirements

Contract Clause/Contract Document reference and description	Work Order specific requirements
<b>Clause 1 - Summary</b> Date for Completion:	<i>June 2018</i>
<b>Clause 5.4.3 – Liquidated damages for delay</b> Amount of liquidated damages for delay in completing by the Date for Completion:	Not applicable.
<b>Clause 7.16 – Building Code</b>	1) Does the Building Code apply to the Contracted Work as there is Commonwealth funding (above the minimum thresholds specified in Schedule 1 of the Building Code) for the Contracted Work <u>or</u> for the project which the Contracted Work forms part of?  Doesn't apply  2) On or after 2 December 2016, has the Contractor or a related entity of the Contractor submitted a response to an expression of interest or tender (howsoever described) for Commonwealth funded Building Work (regardless of whether or not that project was procured by RMS or whether or not the Contractor or the Contractor's related entity were successful)?  No
<b>Clause 7.18 – Aboriginal Participation</b>	
The NSW Government	No

<b>Contract Clause/Contract Document reference and description</b>	<b>Work Order specific requirements</b>
<i>Policy on Aboriginal Participation in Construction</i> applies:	
The Aboriginal Participation Project Category is:	Category <i>[insert number]</i> / Not applicable. <i>[delete whichever is inapplicable, see ECM 5.2.6 for guidance]</i>
The Contractor is required to submit an Aboriginal Participation Plan and Aboriginal Participation Reports	Yes, at times specified in the Contract/No <i>[delete whichever is inapplicable]</i>
The Targeted Project Spend (TPS) at the date of this Work Order is:	\$ <i>[insert amount]</i> (excl GST) / Not Applicable. <i>[delete whichever is inapplicable]</i>
<b>Clause 10.2 &amp; Clause 22.3 of G2 - Chain of Responsibility (CoR) Management Plan</b>  A supplement to the Contractor's CoR Management Plan, to address the chain of responsibilities risks and issues specific to the work or services to be carried out under this Work Order is:.	Not Required



**Issued by Roads and Maritime Services by:**



\_\_\_\_\_  
Signature of issuing officer

Alex Dubois HV Maintenance and Program Officer

Name and position of issuing officer

Date of issue: 01/03/2018

## Euro Civil &amp; Maintenance Pty Ltd

Quality is Our Goal



## Quote

Date	February 28, 2018
PO #	
Quote #	ECMQ00303
Customer ID	RMS

ABN: 26 604 934 698

## Customer:

Roads and Maritime Services

Attention: Alexandre Dubois

ABN: 76 236 371 088

110 George St, Parramatta NSW 2150

(02) 8849 2633

## Quote/Project Description

The works Quote involved the following : Daroobalgie

- 1- Installation of toilet cubicle/meeting room and civil works
- 2- Installation concrete pads for weighbridge at Daroobalgie Sth

	Line Total
<b>1- Installation of toilet cubicle/meeting room and civil works</b>	
Carry out utility surveys and DBYD	
Hiring of 80 meters of water filled barriers to block entry to site Sth bound	
Hiring of 120 meters of temporary fencing for excavated areas around the toilet / change room and concreting lead up pavement	
Hire truck with Hiab (crane) for transportation of cubicle from Westmead NSW to Daroobalgie HVIS	
Hire 5 tone Excavator with auger and rock breaker	
Auger of piers and trenching of footings for new location of site toilet / change room	
Supply Aggregate concrete for piers and footings	
Supply Galvanized steel chains and install in concreted piers for anchorage of cubicle	
Hiring of crane to install cubicle over new footing and anchored down.	
Supply 1 x 3500L Bio Septic tank	
Supply 1x 1100 L pump station	
Supply pf 10,000L Collection Well	
Excavate 25m trench and hole for installation of septic tank in ground	
Supply 100mm sewerage pipes for installation from cubicle to septic tank & overflow	
Trench and excavate from septic tank 25m for installation of overflow retention pit	
Excavate level & compact blinding pad for solid base of rainwater tank	
Supply 90mm storm water piping and plumb up from cubicle to tank	
Supply and install electric water pump to cubicle	
Excavate 100m trench to depth of 600mm	
Supply 100m of 1 inch copper pipe	
Plumb water pipe from water meter to cubicle	
Supply and install 3.5 kw air-conditioning split system as requested to toilet/meeting room	
Excavate and formwork for footpath	
Supply concrete and finish footpath to enter cubicle	
Supply truck & Dog to remove unwanted materials	
Supply 9 cubic meter skip bin for removal of rubbish	
Travel, labor hire, accommodation, fuel and expenses	
<b>2- Installation concrete pads for weighbridge at Daroobalgie Sth</b>	
Carry out utility surveys and DBYD	
Excavation of 15 meters of flexible pavement to a depth of 350mm at Sth Bound	
Formwork 13m long by 6m wide to Nth & Sth Bound for concrete pads	
Supply re-enforced steel mesh and rio bars times two layers to Sth bound weighbridge sites	
Supply approx 20 cubic meters of aggregate to each Nth& Sth bound concrete pads = total of 40 cubes	
Finish concrete and screed to RMS requirements for weighing	
Engage surveyor to ensure concreting together with weighbridge meet the Cat 1 requirements	
Supply truck & Dog to remove unwanted materials	
Supply sweeper to clean site and prep for line marking	
Line Marking the perimeter of the newly installed concrete to match current weighbridge line marking	
Paint 5x5 meters stop sign at the Sth bound sites prior to weighbridge	
Install 2 x stop signs with post before weighbridge	
Travel, labor hire, accommodation, fuel and expenses	
<b>Special Notes and Instructions</b>	
Once signed, please Fax, mail or e-mail it to the provided address.	
Subtotal	\$ 218,750.00
Discount	
Sales Tax Rate	% 10.00
Sales Tax	
Total inc GST	\$ 240,625.00

Above information is not an invoice and only an estimate of services/goods described above.  
Payment will be collected in prior to provision of services/goods described in this quote.

Please confirm your acceptance of this quote by signing this document

Thank you for your business!

Should you have any enquiries concerning this quote, please contact Barry Haden on 7 738

Donaldson St, [Redacted]  
Tel: 7 738 Fax: E-mail: info@ [Redacted]  
BSB: 112879 Account Number [Redacted] 6 088





**CBF PROJECTS pty Ltd**  
**CIVIL BUILDING & FABRICATION**

Elouera Crescent [REDACTED]  
 Telephone: [REDACTED] 8462  
 Mobile: [REDACTED] 4 333  
 ABN: 78 159 482 210

# Quote

Date: March 1, 2018  
 Quote #: Q305

To: Road and Maritime Services

99 Phillip St  
 Parramatta NSW 2150

Mob: [REDACTED] 6 298 Ph: 8837 0636

Fax: 8849 2522

Email: Alex.p.Dubois@rms.nsw.gov.au

ABN 76 236 371 088

Project manager: A. Dubois

**Salesperson**

Chahid Chahine

**Job**

Daroobalgie Inspection station Sth bound

**Payment Terms**

Qty	Unit	Description	Unit Price	Line Total
	EA	<b>Daroobalgie</b> Establishment		
		<b>Amenities Installation</b>		
		<b>Plant Equipment</b>		
		Hiring of Crane for the delivery of Septic tank within the excavated area		
		Truck and Dog for the removal of unwanted materials		
		Hiring of Bobcat with sweeper to clean site once septic and collection well have been installed		
		<b>Concrete</b>		
		Supply and lay concrete for base of septic tank		
		Supply approx 80 cubes of concrete for the weighbridge pads		
		<b>Materials</b>		
		Procure and install steel re-enforced bars to concrete pads		
		Supply Formwork for concrete weighbridge pad and concrete footpath to amenities building		
		Temporary fence all excavated areas - allowance has been made for approx 150m		
		Supply water filled barriers to ensure Nth and Sth bound sites are closed off for the entire work period, approx 14 days has been provisioned		
		supply thermal plastic paint and install 5 x 5 meter stop signs at both Nth and Sth bound sites prior to weighbridge		
		Supply 2 x stop signs with post and install		
		Supply of plumbing materials		
		<b>Installation and civil work</b>		
		DBYD and utility survey checks to be carried out		
		Install plumbing from main to amenity		
		Install 3550L septic tank as per RFQ		
		Install 1100L Pump station as per RFQ		
		Install 10,000L collection well as per RFQ		

[illegible]

OZ CORP CIVIL

## Quote

Luxford Road

DATE March 1, 2018  
Quote # 174

ABN: 37 607 800 895 Phone: 2 468

**Bill To:**Att: Alex Dubois  
Roads and Maritime Services  
110 George Street  
Parramatta NSW 2150  
02 8837 0636**Comments or special instructions:** Darroobalgie South Bound HVIS

Description	AMOUNT
<p>This Quote is for Darroobalgie Heavy Vehicle Inspection Bay</p> <p>Scope of works as per RFQ sent on 26/2/2018</p> <ul style="list-style-type: none"> <li>- Site establishment</li> <li>- Provision of barricading site with temporary fencing and warning signage</li> <li>- Transportation of Amenities to site</li> <li>- Provision of utility surveys</li> <li>- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.</li> </ul> <p>Installation of septic pump tanks as per attached designs and specification at Darroobalgie Sth bound site</p> <ul style="list-style-type: none"> <li>- Installation of amenities block, exact location to be finalized on site by RMS, Indicative location of tanks and blocks shown on attached design</li> <li>- Excavation for council water supply</li> <li>- Connection of water supply by licensed plumber</li> <li>- Excavation and dumping of 30 tonnes of flexible pavement to a depth of 350mm Darroobalgie Sth bound screening lane</li> <li>- Dumping of unwanted materials</li> <li>- Formwork, provisions of steel and concreting 13m long by 6m wide to a depth of 250mm</li> <li>- Line marking of areas around newly installed concrete pad in addition to installation a 5mx5m thermal plastic stop sign on ground prior to weighbridge</li> </ul> <p>Cleaning of site and make good</p> <p>Travel Allowances + incidentals</p> <p>Accommodation</p>	
<b>TOTAL Ex GST</b>	\$ 225,000.00
<b>TOTAL Inc. GST</b>	\$ 247,500.00

If you have any questions concerning this quotation, KrisTui, 2 468, E-mail: admin

THANK YOU FOR YOUR BUSINESS!



## FW: daroobalgie sth euro

---

**From:** DUBOIS Alexandre </o=rta/ou=exchange administrative group (fydibohf23spdl)/cn=recipients/cn=alexandu">  
**To:** TSS.RMSContracts <tss.rmscontracts@transport.nsw.gov.au>  
**Date:** Thu, 01 Mar 2018 17:19:27 +1100  
**Attachments:** IGA\_1\_3\_2018\_17\_1\_25\_348.pdf (477.21 kB)

---

Good afternoon,

Can you please assist in creating the PO for the attached request

Thank you

-----Original Message-----

From: iga@rms.nsw.gov.au [mailto:iga@rms.nsw.gov.au]  
Sent: Thursday, 1 March 2018 5:02 PM  
To: DUBOIS Alexandre  
Subject: daroobalgie sth euro

Scan attached



## Roads and Maritime Services

### Contract Creation & Variation

Is this a CM21 contract? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	Request type: <input checked="" type="checkbox"/> Create new <input type="checkbox"/> Amend existing
--	--

#### Contract variation ONLY details

For contract variation only. Please tick as applicable and fill in details below as required.

<input type="checkbox"/> New value <input type="checkbox"/> New date	Equip purchase order number OR contract number:
--	--

#### Contract details

Supplier: Euro Civil and Maintenance	Supplier No.:
Vendor ABN: 26 604 934 698	
Does the Contract require ERS/RCTI? (PO purposes)	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No
Contract title: (Please include CM21 number on the title of CM21 contracts)	Concrete, Civil works on Newell Highway Sth bound WHS issues
Effective date: 1 Mar 2018	Expiry date: 30 Jun 2018
Contract type:	<input type="checkbox"/> Council <input checked="" type="checkbox"/> CM21 <input type="checkbox"/> Discrete <input type="checkbox"/> Supply Agreement <input checked="" type="checkbox"/> Panel
Payment terms: 30 days from the date of invoice Category:	
<input type="checkbox"/> Payment claim under Security & Payment Act (15 day payment term - SOPA)	

#### Financial details

Awarded amount (ex GST): \$218,750	Initial contract amount:
Contract contingency (if applicable):	Expenditure type: Capex
Total Contract amount (Awarded amount + Contingency): \$218,750	Hierarchical type: Panel
Material Group (UNSPSC product category): 72000000	
Variation amount (excluding approved contract value):	
WBS code: P.0018688.29	Cost centre: 2935
G/L code: 513140	
Agency:	<input type="checkbox"/> Cluster wide – 9000 <input type="checkbox"/> TfNSW – 1000 <input checked="" type="checkbox"/> RMS – 3000
Purchasing group (Region): Sydney	
Notice period (in days) 30 days by default:	
Requesting/Requesting officer name: Alexandre Dubois	

#### Internal stakeholder details

Initiator (Business sponsor):
Contract manager: Alexandre Dubois
Procurement owner: Alexandre Dubois
Contractor stakeholder visibility (Team Tab):

**CLID line item details – Min. requirement of 1 line (\* Mandatory fields)**

<b>Name Line #1</b> (max 40 character limit)* Concrete, Civil works on Newell Highway Sth bound WHS issues			
Description*:			
Unit of measure*:	Each	Target quantity*:	1.0
		Price:	\$218,750
Long text*:			
Supplier part no.*:		Material Group (UNSPSC product category):	

<b>Name Line #2</b> (max 40 character limit)*			
Description*:			
Unit of measure*:		Target quantity*:	
		Price:	
Long text*:			
Supplier part no.*:		Material Group (UNSPSC product category):	

<b>Name Line #3</b> (max 40 character limit)*			
Description*:			
Unit of measure*:		Target quantity*:	
		Price:	
Long text*:			
Supplier part no.*:		Material Group (UNSPSC product category):	

**To be completed only if any other form of approval documentation not attached such as "Letter of Acceptance"**

<b>Requested by :</b> Requester <b>cannot</b> be a Business Partner		<b>Delegated Approval by:</b> Delegation <b>must</b> cover the total value of the PO	
Name: Alexandre Dubois		Name: Craig Steyn	
Staff ID:	00965213	Staff ID:	00961247
Position: Heavy Vehicle Project & Support Officer		Delegation Level:	4
Phone No: 02 8837 0636		Position: Manager Heavy Vehicle Programs	
Signature: 		Phone No: 02 8837 0687	
Date:	1/3/18	Signature*: 	Date: 1.3.2018

**Guidelines**

<p>This form must be used for:</p> <ul style="list-style-type: none"> <li>Creation and variation of all types of contracts in Equip for RMS</li> <li>Variation of purchase orders attached to a contract in Equip</li> </ul> <p>All fields are mandatory unless stated "as applicable". Documentation to be attached with the contracts are:</p> <ul style="list-style-type: none"> <li>Letter of acceptance</li> <li>Tender assessment report</li> <li>Pricing schedules</li> </ul> <p>The form along with the documentation should be forwarded to <a href="mailto:TSS.RMSContracts@transport.nsw.gov.au">TSS.RMSContracts@transport.nsw.gov.au</a></p>
---

For assistance in the completion of these forms please contact [TSS.RMSContracts@transport.nsw.gov.au](mailto:TSS.RMSContracts@transport.nsw.gov.au)

## Disclosure of Information

Class 1 Contract	
Contract No/ID :	17.0000302935.1100-0034
Equip Contract No :	17.0000302935.1100
Contract Description :	Panel for HVEP- WHS items Newell Hwy Enforcement site
Contract Commencement Date :	01/03/2018
Period of Contract:	20 weeks
Contractor:	EURO CIVIL & MAINTENANCE PTY LTD
Contractor Address:	EURO CIVIL & MAINTENANCE PTY LTD, [REDACTED] Donaldson Street, [REDACTED]
Trading Name:	
Trading Name Address:	
Estimated Payable (\$ Incl GST) :	\$ 240,625.00
Method of Tendering:	Limited (Single Invitation / Selective/WADs)

- Particulars of any related body corporate (within the meaning of the Corporations Act 2001 of the Commonwealth) in respect of the contractor, or any other private sector entity in which the contractor has an interest, that will be involved in carrying out any of the contractor's obligations under the contract or will receive a benefit under the contract

NA

- A description of any provisions under which the amount payable to the contractor may be varied

No provisions under which the amount payable to the contractor may be varied

- A description of any provisions with respect to the renegotiation of the contract

No provisions with respect to the renegotiation of the contract

- In the case of a contract arising from a tendering process, a summary of the criteria against which the various tenders were assessed

Price, experience, panel contractor

- A description of any provisions under which it is agreed that the contractor is to receive payment for providing operational or maintenance services

NA

- **The reason why the contract has provisions which exclude or modify application of Part 4 Proportionate liability of the Civil**

NA

---

## Work Order 17.0000302935.1100-0015

This document is a Work Order issued under your Work-as-Ordered Contract with RMS dated 31/10/2017 for the Installation of Amenities Block and Civil works at Daroobalgie HVIS.

Under this Work Order, you are requested to carry out the work or services described below ('Contracted Work') on the terms of your Work-as-Ordered Contract and this Work Order.

### **Contracted Work**

Roads and Maritime sought through an RFQ sent on the 26<sup>th</sup> of feb 2018 the submission of a lump sum fee estimate for the installation of Amenities block and the concrete of pavement on the approach to the weighbridge at Daroobalgie HVIS Sth bound on the Newell High way.

The works involve the following:

- Transportation of Amenities to site
- Utility surveys
- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.
- Installation of Septic pump tanks as per attached designs and specifications at Daroobalgie Nth bound site.
- Installation of amenities block, exact location to be finalised on site by RMS, indicative location of tanks and block shown on attached design.
- Excavation for council water supply
- Dumping of unwanted materials
- Connection of water supply by a licenced plumber.
- Excavation and dumping of 15 meters of flexible pavement to a depth of 350mm and allowance for dumping costs at both Daroobalgie Nth and Sth.
- Formwork, provision of steel and concreting 13m long by 6 m wide to a depth of 250mm, cross section drawing to be provided at both Daroobalgie Nth and Sth.
- Line marking of areas around the newly installed concrete pad in addition to the installation a 5mx5m stop sign at both Nth and Sth bound sites prior to the weighbridge.( Current stop marker is faded)
- Installation of two stop signs with posts
- Cleaning of the area and make good.

## Work Order Specific Requirements

Contract Clause/Contract Document reference and description	Work Order specific requirements
<b>Clause 1 - Summary</b> Date for Completion:	<i>June 2018</i>
<b>Clause 5.4.3 – Liquidated damages for delay</b> Amount of liquidated damages for delay in completing by the Date for Completion:	Not applicable.
<b>Clause 7.16 – Building Code</b>	1) Does the Building Code apply to the Contracted Work as there is Commonwealth funding (above the minimum thresholds specified in Schedule 1 of the Building Code) for the Contracted Work <u>or</u> for the project which the Contracted Work forms part of?  Doesn't apply  2) On or after 2 December 2016, has the Contractor or a related entity of the Contractor submitted a response to an expression of interest or tender (howsoever described) for Commonwealth funded Building Work (regardless of whether or not that project was procured by RMS or whether or not the Contractor or the Contractor's related entity were successful)?  No
<b>Clause 7.18 – Aboriginal Participation</b>	
The NSW Government	No

<b>Contract Clause/Contract Document reference and description</b>	<b>Work Order specific requirements</b>
<i>Policy on Aboriginal Participation in Construction</i> applies:	
The Aboriginal Participation Project Category is:	Category <i>[insert number]</i> / Not applicable. <i>[delete whichever is inapplicable, see ECM 5.2.6 for guidance]</i>
The Contractor is required to submit an Aboriginal Participation Plan and Aboriginal Participation Reports	Yes, at times specified in the Contract/No <i>[delete whichever is inapplicable]</i>
The Targeted Project Spend (TPS) at the date of this Work Order is:	\$ <i>[insert amount]</i> (excl GST) / Not Applicable. <i>[delete whichever is inapplicable]</i>
<b>Clause 10.2 &amp; Clause 22.3 of G2 - Chain of Responsibility (CoR) Management Plan</b>  A supplement to the Contractor's CoR Management Plan, to address the chain of responsibilities risks and issues specific to the work or services to be carried out under this Work Order is:.	Not Required

**Issued by Roads and Maritime Services by:**



\_\_\_\_\_  
Signature of issuing officer

Alex Dubois HV Maintenance and Program Officer

Name and position of issuing officer

Date of issue: \_\_\_\_01/03/2018\_\_\_\_



## Euro Civil &amp; Maintenance Pty Ltd

Quality is Our Goal



ABN: 26 604 934 698

## Customer:

Roads and Maritime Services

Attention: Alexandre Dubois

ABN: 76 236 371 088

110 George St, Parramatta NSW 2150  
(02) 8849 2633

Date: February 28, 2018  
PO #:   
Quote #: ECMQ00303  
Customer ID: RMS

## Quote

## Quote/Project Description

The works Quote involved the following : Daroobalgie

- 1- Installation of toilet cubicle/meeting room and civil works
- 2- Installation concrete pads for weighbridge at Daroobalgie Sth

## 1- Installation of toilet cubicle/meeting room and civil works

Carry out utility surveys and DBYD  
Hiring of 80 meters of water filled barriers to block entry to site Sth bound  
Hiring of 120 meters of temporary fencing for excavated areas around the toilet / change room and concreting lead up pavement  
Hire truck with Hiab (crane) for transportation of cubicle from Westmead NSW to Daroobalgie HVIS  
Hire 5 tone Excavator with auger and rock breaker  
Auger of piers and trenching of footings for new location of site toilet / change room  
Supply Aggregate concrete for piers and footings  
Supply Galvanized steel chains and install in concreted piers for anchorage of cubicle  
Hiring of crane to install cubicle over new footing and anchored down.  
Supply 1 x 3500L Bio Septic tank  
Supply 1x 1100 L pump station  
Supply pf 10,000L Collection Well  
Excavate 25m trench and hole for installation of septic tank in ground  
Supply 100mm sewerage pipes for installation from cubicle to septic tank & overflow  
Trench and excavate from septic tank 25m for installation of overflow retention pit  
Excavate level & compact blinding pad for solid base of rainwater tank  
Supply 90mm storm water piping and plumb up from cubicle to tank  
Supply and install electric water pump to cubicle  
Excavate 100m trench to depth of 600mm  
Supply 100m of 1 inch copper pipe  
Plumb water pipe from water meter to cubicle  
Supply and install 3.5 kw air-conditioning split system as requested to toilet/meeting room  
Excavate and formwork for footpath  
Supply concrete and finish footpath to enter cubicle  
Supply truck & Dog to remove unwanted materials  
Supply 9 cubic meter skip bin for removal of rubbish  
Travel, labor hire, accommodation, fuel and expenses

## 2- Installation concrete pads for weighbridge at Daroobalgie Sth

Carry out utility surveys and DBYD  
Excavation of 15 meters of flexible pavement to a depth of 350mm at Sth Bound  
Formwork 13m long by 6m wide to Nth & Sth Bound for concrete pads  
Supply re-enforced steel mesh and rio bars times two layers to Sth bound weighbridge sites  
Supply approx 20 cubic meters of aggregate to each Nth & Sth bound concrete pads = total of 40 cubes  
Finish concrete and screed to RMS requirements for weighing  
Engage surveyor to ensure concreting together with weighbridge meet the Cat 1 requirements  
Supply truck & Dog to remove unwanted materials  
Supply sweeper to clean site and prep for line marking  
Line Marking the perimeter of the newly installed concrete to match current weighbridge line marking  
Paint 5x5 meters stop sign at the Sth bound sites prior to weighbridge  
Install 2 x stop signs with post before weighbridge  
Travel, labor hire, accommodation, fuel and expenses

## Special Notes and Instructions

Once signed, please Fax, mail or e-mail it to the provided address.

Subtotal	\$	218,750.00
Discount		
Sales Tax Rate	%	10.00
Sales Tax		
Total inc GST	\$	240,625.00

Above information is not an invoice and only an estimate of services/goods described above.  
Payment will be collected in prior to provision of services/goods described in this quote.

Please confirm your acceptance of this quote by signing this document

Thank you for your business!

Should you have any enquiries concerning this quote, please contact Barry Haden on 7 738

Donaldson St.  
Tel: 7 738 Fax: E-mail: info@  
BSB: 112879 Account Number 6 088





**CBF PROJECTS Pty Ltd**  
**CIVIL BUILDING & FABRICATION**

Elouera Crescent [REDACTED]  
 Telephone: [REDACTED] 8462  
 Mobile: [REDACTED] 4 333

ABN: 78 159 482 210

# Quote

Date: March 1, 2018  
 Quote #: Q305

To: Road and Maritime Services

99 Phillip St  
 Parramatta NSW 2150  
 Mob: [REDACTED] 6 298 Ph: 8837 0636 Fax: 8849 2522  
 Email: Alex.p.Dubois@rms.nsw.gov.au  
 ABN 76 236 371 088

Project manager: A. Dubois

Salesperson	Job	Payment Terms
Chahid Chahine	Daroobalgie Inspection station Sth bound	

Qty	Unit	Description	Unit Price	Line Total
	EA	<b>Daroobalgie</b> Establishment		
		<b>Amenities Installation</b>		
		<b>Plant Equipment</b>		
		Hiring of Crane for the delivery of Septic tank within the excavated area		
		Truck and Dog for the removal of unwanted materials		
		Hiring of Bobcat with sweeper to clean site once septic and collection well have been installed		
		<b>Concrete</b>		
		Supply and lay concrete for base of septic tank		
		Supply approx 80 cubes of concrete for the weighbridge pads		
		<b>Materials</b>		
		Procure and install steel re-enforced bars to concrete pads		
		Supply Formwork for concrete weighbridge pad and concrete footpath to amenities building		
		Temporary fence all excavated areas - allowance has been made for approx 150m		
		Supply water filled barriers to ensure Nth and Sth bound sites are closed off for the entire work period, approx 14 days has been provisioned		
		supply thermal plastic paint and install 5 x 5 meter stop signs at both Nth and Sth bound sites prior to weighbridge		
		Supply 2 x stop signs with post and install		
		Supply of plumbing materials		
		<b>Installation and civil work</b>		
		DBYD and utility survey checks to be carried out		
		Install plumbing from main to amenity		
		Install 3550L septic tank as per RFQ		
		Install 1100L Pump station as per RFQ		
		Install 10,000L collection well as per RFQ		

[illegible]

**OZ CORP CIVIL****Quote**

Luxford Road

**DATE** March 1, 2018  
**Quote #** 174

ABN: 37 607 800 895 Phone: 2 468

**Bill To:**Att: Alex Dubois  
Roads and Maritime Services  
110 George Street  
Parramatta NSW 2150  
02 8837 0636**Comments or special instructions:** Darroobalgie South Bound HVIS

Description	AMOUNT
<p>This Quote is for Darroobalgie Heavy Vehicle Inspection Bay</p> <p>Scope of works as per RFQ sent on 26/2/2018</p> <ul style="list-style-type: none"> <li>- Site establishment</li> <li>- Provision of barricading site with temporary fencing and warning signage</li> <li>- Transportation of Amenities to site</li> <li>- Provision of utility surveys</li> <li>- Provision of plant equipment which includes, Excavator, truck with Hiab, sweeper and bobcat.</li> </ul> <p>Installation of septic pump tanks as per attached designs and specification at Darroobalgie Sth bound site</p> <ul style="list-style-type: none"> <li>- Installation of amenities block, exact location to be finalized on site by RMS, Indicative location of tanks and blocks shown on attached design</li> <li>- Excavation for council water supply</li> <li>- Connection of water supply by licensed plumber</li> <li>- Excavation and dumping of 30 tonnes of flexible pavement to a depth of 350mm Darroobalgie Sth bound screening lane</li> <li>- Dumping of unwanted materials</li> <li>- Formwork, provisions of steel and concreting 13m long by 6m wide to a depth of 250mm</li> <li>- Line marking of areas around newly installed concrete pad in addition to installation a 5mx5m thermal plastic stop sign on ground prior to weighbridge</li> </ul> <p>Cleaning of site and make good</p> <p>Travel Allowances + incidentals</p> <p>Accommodation</p>	
<b>TOTAL Ex GST</b>	<b>\$ 225,000.00</b>
<b>TOTAL Inc. GST</b>	<b>\$ 247,500.00</b>

If you have any questions concerning this quotation, KrisTui, 2 468, E-mail: admin

**THANK YOU FOR YOUR BUSINESS!**



## CW2304176 - 17.0000302935.1100.0034 Daroobalgie WHS: Approval by Contract Approver was fully approved.

---

**From:** "@customerresources/DefaultNotification" <no-reply@ansmtp.riba.com>  
**To:** DUBOIS Alexandre <alex.p.dubois@rms.nsw.gov.au>  
**Date:** Tue, 06 Mar 2018 08:58:47 +1100

---

CW2304176 - 17.0000302935.1100.0034 Daroobalgie WHS: Approval by Contract Approver was fully approved.

**Task Title:** Approval by Contract Approver

**Task Description:** Task for TSS review and approval for contract establishment and amendment

You are being sent this email because you are the owner of a task that has been approved by all people in the approval flow.

This email originated from the Ariba system used by Transport NSW and was originally sent to: ALEX.P.DUBOIS@RMS.NSW.GOV.AU

System Reference: [Click Here](#) to access the system.

## Fwd: Notification Purchase Order Creation

---

**From:** alex.p.dubois@rms.nsw.gov.au  
**To:** info@[REDACTED]  
**Date:** Wed, 07 Mar 2018 12:35:14 +1100

---

Sent from my iPhone

Begin forwarded message:

**From:** DoNotReply <[donotreply@transport.nsw.gov.au](mailto:donotreply@transport.nsw.gov.au)>  
**Date:** 7 March 2018 at 12:15:23 pm AEDT  
**To:** DUBOIS Alexandre <[Alex.p.Dubois@rms.nsw.gov.au](mailto:Alex.p.Dubois@rms.nsw.gov.au)>  
**Subject:** Notification Purchase Order Creation

Hello Alexandre Dubois  
 Purchase Order 4200044014 has been created and released for supplier EURO CIVIL & MAINTENANCE PTY LTD ( 0020012410 )

Associated Contract:

Purchase Order: 4200044014  
 Purchase Order Date:07.MAR.2018

Purchase Order Total Value: 218750.00 AUD  
 Purchase Order Tax Value : 21875.00 AUD  
 Purchase Order Gross Total: 240625.00 AUD  
 Purchase Order Delivery Address:RMS OFFICE OF CHIEF EXECUTIVE, 28 ENNIS ROAD,  
 MILSONS POINT NSW 2061, AUSTRALIA

Line No	Item Curr	Item Value	Item Quantity	Item UoM	Item Short Text
00010	AUD	218750.00	1.000	AU	17.0000302935.1100.0034
Daroobalgie WHS					

If the above details are incorrect, please contact TSS Purchase Orders  
 ([tss.purchaseorders@transport.nsw.gov.au](mailto:tss.purchaseorders@transport.nsw.gov.au)).

You can view the status of your Shopping Cart by logging into Transport Equip.



## Fwd: Old Daroobalgie survey weighbridge

---

**From:** info <info@[REDACTED]>  
**To:** DUBOIS Alexandre <alex.p.dubois@rms.nsw.gov.au>  
**Date:** Thu, 12 Apr 2018 08:12:10 +1000  
**Attachments:** Daroobalgie Old Survey weighbridge SOUTHBOUND.pdf (59.5 kB)

---

Sent from my Samsung Galaxy smartphone.

----- Original message -----

**From:** Ronny <precisesurveying@gmail.com>  
**Date:** 12/4/18 5:53 am (GMT+10:00)  
**To:** info@eurocandm.com.au  
**Subject:** Old Daroobalgie survey weighbridge

Kind Regards


Ronny Elzahr

Director

Mob: [REDACTED] 55 25

Ph: (02) 9620 2133

Email: [precisesurveying@gmail.com](mailto:precisesurveying@gmail.com)

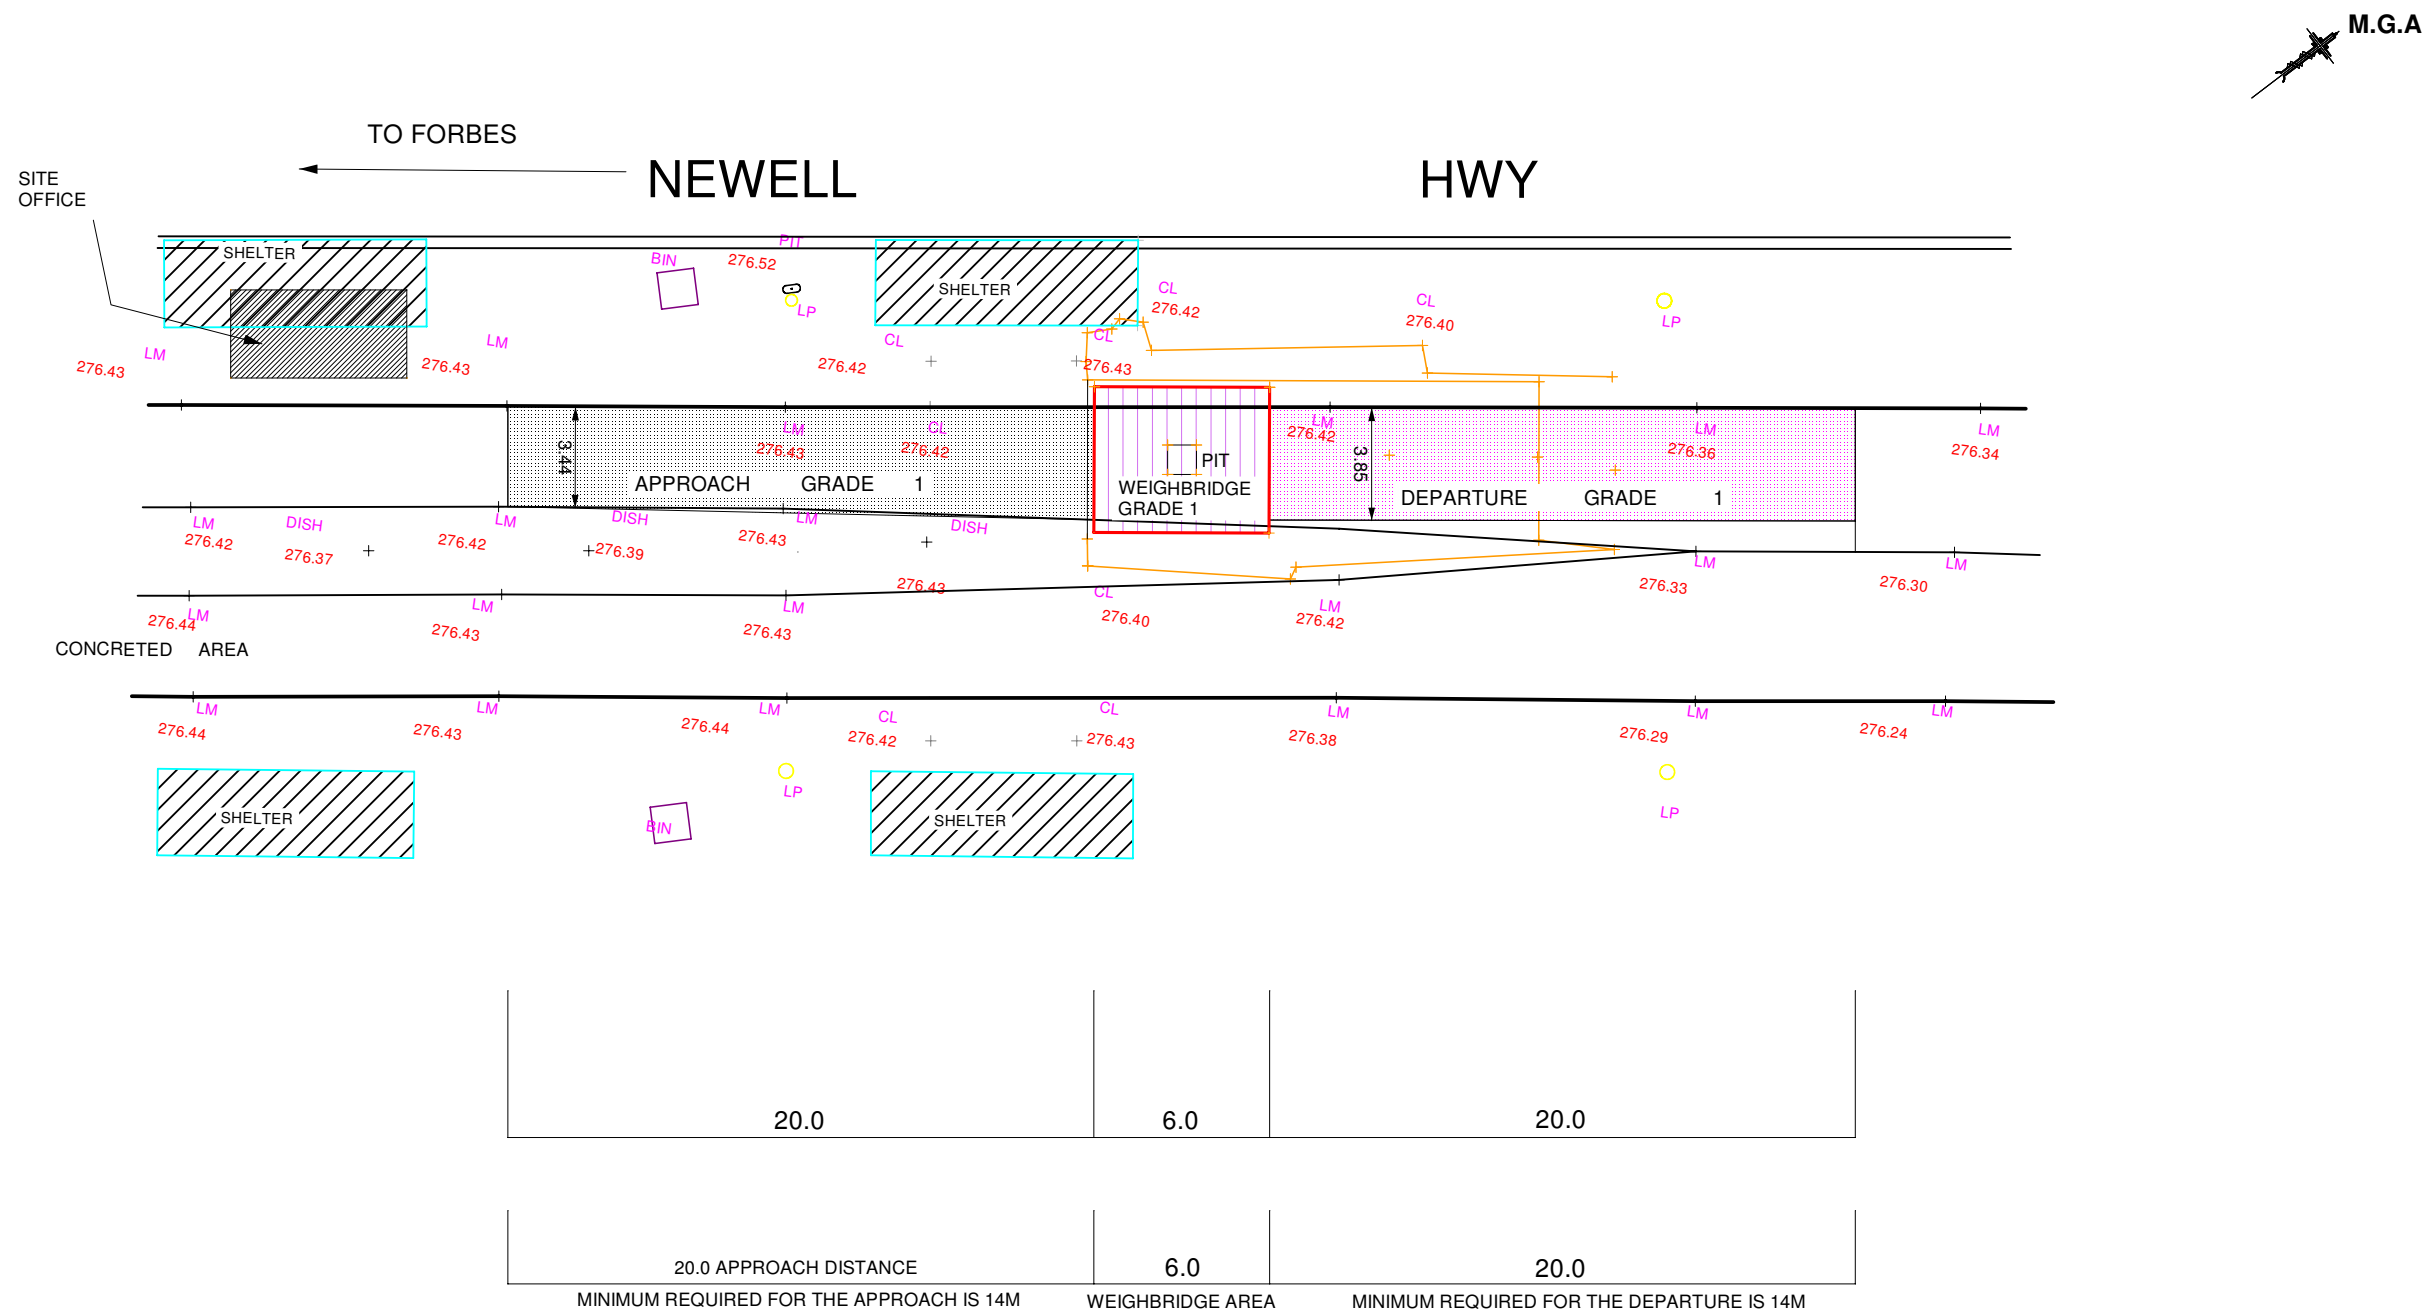

AMENDMENTS		<div>NOTES: IF ANY CONSTRUCTION WORK IS PLANNED THE CONCERNED SHOULD UNDERTAKE A FURTHER SURVEY TO DEFINE ANY BOUNDARIES AS NO BOUNDARIES HAVE BEEN DEFINED. ANY POINT CRITICAL TO THE PREPARATION OF PLANS AND/OR CONSTRUCTION SHOULD BE CHECKED BY THE BUILDER/ARCHITECT BEFORE ANY WORK COMMENCING. ALL SERVICES ARE INDICATIVE ONLY. OTHER SERVICES MAY EXIST. ALL TREES ARE APPROXIMATE SIZE AND LOCATION ONLY. DIAL BEFORE YOU DIG SHOULD BE UNDERTAKEN PRIOR TO ANY EXCAVATION WORK ON 1100. PRIOR TO THE COMPLETION OF ANY PLANS AND/OR CONSTRUCTION FURTHER FIELD WORK SHOULD BE UNDERTAKEN.</div>	<div><div><div></div><div>PRECISE SURVEYING</div><div>PTY LTD</div></div><div><div>MOB: 0415 55 55 25</div><div>PO BOX 145 HORSLEY PARK 2175</div><div>EMAIL: <a href="mailto:precisesurveying@gmail.com">precisesurveying@gmail.com</a></div></div></div>	CLIENT: RMS		JOB No: DAROOBALGIE
DATE:	DESCRIPTION:		CLIENT ADDRESS:		JOB ADDRESS: WEIGHBRIDGE NEWELL HWY SOUTHBOUND DAROOBALGIE 2018	
			SCALE: N/A		LEVELS: AHD	
						DATE: 10.04.2018

## FW: ECM Claim for payment Daroobalgie Sth

---

**From:** DUBOIS Alexandre <alex.p.dubois@rms.nsw.gov.au>  
**To:** TSS Invoices <tss.invoices@transport.nsw.gov.au>  
**Date:** Thu, 28 Jun 2018 12:13:48 +1000

---

**From:** info@eurocandm.com.au [mailto:info@eurocandm.com.au]  
**Sent:** Friday, 8 June 2018 12:18 PM  
**To:** DUBOIS Alexandre  
**Subject:** ECM Claim for payment Daroobalgie Sth

Hi Alex

Please find Claim for payment attached for the completed works

Kind Regards,

Barry Haden  
 Director

■ Donaldson St Bradbury NSW  
 2560 Australia  
 E: [info@eurocandm.com.au](mailto:info@eurocandm.com.au)  
 M: +61 ■ 7 738

This email is confidential and intended solely for the use of the individual to whom it is addressed. Any views or opinions presented are solely those of the author and do not necessarily represent those of ECM. If you are not the intended recipient, please be advised that forwarding, printing or copying of this email is strictly prohibited. If you have received this email in error please notify our admin on +61 ■ 7 738

This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.

 **Consider the environment. Please don't print this e-mail unless really necessary.**



## Euro Civil &amp; Maintenance Pty Ltd

Quality is Our Goal



## CLAIM FOR PAYMENT

Date	June 7, 2018
PO #	4200044014
Claim #	ECM1177
Customer ID	RMS

ABN: 26 604 934 698

## Customer:

Roads and Maritime Services

Attention: Alexandre Dubois

ABN: 76 236 371 088

110 George St, Parramatta NSW 2150

## Quote/Project Description

The works Claim involved the following : Daroobalgie

1- Installation of toilet cubicle/meeting room and civil works

2- Installation concrete pads for weighbridge at Daroobalgie Sth

	Line Total
<b>1- Installation of toilet cubicle/meeting room and civil works</b>	
Carry out utility surveys and DBYD	
Hiring of 80 meters of water filled barriers to block entry to site Sth bound	
Hiring of 120 meters of temporary fencing for excavated areas around the toilet / change room and concreting lead up pavement	
Hire truck with Hiab (crane) for transportation of cubicle from Westmead NSW to Daroobalgie HVIS	
Hire 5 tone Excavator with auger and rock breaker	
Auger of piers and trenching of footings for new location of site toilet / change room	
Supply Aggregate concrete for piers and footings	
Supply Galvanized steel chains and install in concreted piers for anchorage of cubicle	
Hiring of crane to install cubicle over new footing and anchored down.	
Supply 1 x 3500L Bio Septic tank	
Supply 1x 1100 L pump station	
Supply pf 10,000L Collection Well	
Excavate 25m trench and hole for installation of septic tank in ground	
Supply 100mm sewerage pipes for installation from cubicle to septic tank & overflow	
Trench and excavate from septic tank 25m for installation of overflow retention pit	
Excavate level & compact blinding pad for solid base of rainwater tank	
Supply 90mm storm water piping and plumb up from cubicle to tank	
Supply and install electric water pump to cubicle	
Excavate 100m trench to depth of 600mm	
Supply 100m of 1 inch copper pipe	
Plumb water pipe from water meter to cubicle	
Supply and install 3.5 kw air-conditioning split system as requested to toilet/meeting room	
Excavate and formwork for footpath	
Supply concrete and finish footpath to enter cubicle	
Supply truck & Dog to remove unwanted materials	
Supply 9 cubic meter skip bin for removal of rubbish	
Travel, labor hire, accommodation, fuel and expenses	
<b>2- Installation concrete pads for weighbridge at Daroobalgie Sth</b>	
Carry out utility surveys and DBYD	
Excavation of 15 meters of flexible pavement to a depth of 350mm at Sth Bound	
Formwork 13m long by 6m wide to Nth & Sth Bound for concrete pads	
Supply re-enforced steel mesh and rio bars times two layers to Sth bound weighbridge sites	
Supply approx 20 cubic meters of aggregate to each Nth& Sth bound concrete pads = total of 40 cubes	
Finish concrete and screed to RMS requirements for weighing	
Engage surveyor to ensure concreting together with weighbridge meet the Cat 1 requirements	
Supply truck & Dog to remove unwanted materials	
Supply sweeper to clean site and prep for line marking	
Line Marking the perimeter of the newly installed concrete to match current weighbridge line marking	
Paint 5x5 meters stop sign at the Sth bound sites prior to weighbridge	
Install 2 x stop signs with post before weighbridge	
Travel, labor hire, accommodation, fuel and expenses	
<b>Special Notes and Instructions</b>	
Once signed, please Fax, mail or e-mail it to the provided address.	
Subtotal	\$ 218,750.00
Discount	
Sales Tax Rate	% 10.00
Sales Tax	
<b>Total inc GST</b>	<b>\$ 240,625.00</b>

Payment will be collected in prior to provision of services/goods described in this quote.

Signature

Print Name

Date

Thank you for your business!

Should you have any enquiries concerning this Claim, please contact Barry Haden on 7 738

Donaldson St, 7 738 Fax: E-mail: info@  
 BSB: 112879 Account Number : 6 088
